


Project : Atlas Superclub

Ref : No. BKD/ASC/Payment/011

Date 22 February 2026

Subject : Request for payment of the 11nd Final Claim VO of Final Account SI-050

Description : Payment No.11

Type Of Work : Payment

Attached : ☒ 1. Letter , 2. Summary payment No.11
☐ 3. S-Curve , 4. Advancement Photos

Others :
Remark :
Attn : CMP Management Asia Co., Ltd. (CMP)

- ☐ For Designer Opinion ☒ For Approval
☐ For Information ☐ See notes

Notes
From : Bangkok Dec-Con Public Company Limited

Signature :

(Mr. Thanapon Wittayaphon)

Project Manager

Date : 22 February, 2026 **Time :**
Attn : Owner/Designer.....

- ☐ For comment ☐ For Approval
☐ For Information ☐ See notes

Notes
From : CMP Management Asia Co., Ltd.

Signature :

()

Project Manager / CMP

Date : **Time :**
Attn : CMP Management Asia Co., Ltd.

- ☐ Approval ☐ Approval As Noted
☐ Resubmit ☐ Not Approved

Notes
From : Owner/Designer

Signature :

()

Project Manager / Designer

Date : **Time :**
Attn : Bangkok Dec-Con Public Company Limited

- ☐ Approval ☐ Approval As Noted
☐ Resubmit ☐ Not Approved

Notes
From : CMP Management Asia Co., Ltd.

Signature :

()

Project Manager / CMP

Date : **Time :**

cc.

☐ Original(ITD)

☐ HWG

☐ CMP

☐ Designer



บริษัท บางกอก เดค-คอน จำกัด (มหาชน)

BANGKOK DEC-CON PUBLIC CO., LTD.

52/3 หมู่ 8 ถนนบางบัวทอง-สุพรรณบุรี ตำบลละหาร อำเภอบางบัวทอง จังหวัดนนทบุรี 11110

52/3 Moo.8 Bangbuathong-Suphanburi Road, T.LahanBangbuathong, Nonthaburi, Thailand 11110

เลขประจำตัวผู้เสียภาษี 0107554000178สำนักงานใหญ่

ใบส่งสินค้า/ใบแจ้งหนี้

Invoice/ Billing

ลูกค้า : (00445)บริษัท รัชดา เอ็นเตอร์เทนเมนท์ กรุ๊ป จำกัด สำนักงานใหญ่ Customer เลขที่ 58 ถนนรัชดาภิเษก ซอย 4 แขวงห้วยขวาง เขตห้วยขวาง กรุงเทพมหานคร 10310 Tel. Fax. Tax ID : 0105566107710	เลขที่ : IB6902010 No. วันที่ : 24/02/2026 Date
---	--

เลขที่เอกสารอ้างอิง Ref. Document	วันที่ Date	เลขที่ใบสั่งซื้อ/สัญญา P.O. No./Contract No.	เงื่อนไขชำระเงิน Term of Payment	วันครบกำหนด Due Date	Progress Payment
	24/02/2026		0	24/02/2026	

โครงการ Atlas Superclub (SPC)
Project

ลำดับ Item	รายการ Description	จำนวน/หน่วย Quantity/Unit	หน่วย Unit	ราคาต่อหน่วย Unit Price	จำนวนเงิน Amount
---------------	-----------------------	------------------------------	---------------	----------------------------	---------------------

1	รายได้จากการดกนส่งกานใน Interim Payment No.2 VO of Final Account SI-050 PROJECT ATLAS SUPERCLUB	1	งาน	675,998.40	675,998.40
---	---	---	-----	------------	------------

จำนวนเงินรวมทั้งสิ้น	723,318.29	จำนวนเงินรวม	675,998.40
หัก เงินประกันผลงาน (Less Retention) 5.00%	33,799.92	หัก เงินจ่ายล่วงหน้า (Less Advance)	0.00
มูลค่างานคงเหลือ (Contract Value Balance)	689,518.37	รวมเงิน TOTAL	675,998.40
หัก ณ ที่จ่าย (Withholding Tax) 3.00%	20,279.95	ภาษีมูลค่าเพิ่ม 7.00%	47,319.89
จำนวนสุทธิ (Net Amount)	669,238.42	Value Added Tax	

(เจ็ดแสนสองหมื่นสามพันสามร้อยสิบแปดบาทสี่สิบเก้าสตางค์)	จำนวนเงินรวมทั้งสิ้น Total Amount	723,318.29
---	--------------------------------------	------------

- หมายเหตุ 1. โปรดส่งจ่ายเช็คขีดคร่อมในนาม บริษัท บางกอก เดค-คอน จำกัด (มหาชน) และขีด " หรือผู้ถือ " ออก " .
2. ได้รับสินค้าและบริการดังรายการข้างบนนี้ไว้โดยถูกต้องครบถ้วนแล้ว

บริษัท ผู้จัดทำ 24 FEB 2026 วันที่	บริษัท ผู้รับงาน BANGKOK DEC - CON PUBLIC COMPANY LIMITED วันที่	บริษัท บางกอก เดค-คอน จำกัด (มหาชน) BANGKOK DEC-CON PUBLIC CO., LTD. ผู้รับงาน 24 FEB 2026 วันที่
---	--	---



Bangkok Dec-Con Public Company Limited

52/3 Moo 8, Bangbuatong-Supanburi Road La Han Sub-District

Bang Bua Thong District Nonthaburi, 11110. Thailand

TAX.ID 0107554000178

Project : ATLAS SUPERCLUB @ Ratchada Soi 4

Claim VO. No. 2 VO of Final Account SI-050

12 February 2026

INVOICE

Customer Ratchada Entertainment Group Co., Ltd. TAX ID. 0105566107710

Address 58 Ratchadaphisek Road, Soi 4, Huaykhwang Subdistrict,
Huaykhwang District, Bangkok, Thailand 10310

No.	Description	Amount
A	Interim Payment No.2 VO of Final Account SI-050	675,998.40
B	Less Advance Payment 40%	-
C	Total Payment	675,998.40
D	Less Retention 5%	33,799.92
E	Total	642,198.48
F	VAT 7%	47,319.89
G	Total Payment (Include VAT)	689,518.37
H	Less Withholding Tax 3%	20,279.95
I	Net Payment	669,238.42

(Six hundred sixty-nine thousand two hundred thirty-eight Baht and forty-two Satang.).

Authorized Signature

(Mr. Thanapon Wittayaphon)

Project Manager

Item	Description	Unit	Contract			Previous Period Claim		This month Claim		Cumulative to date		Remaining Balances	
			QTY.	BKD	%	Total	%	Total	%	Total	%	Total	%
	Summary of construction costs of the project.												
A	SI-050 - Conclusion of all VO	LS	1	675,998.40	100.00%	-	0.00%	675,998.40	100.00%	675,998.40	100.00%	-	0.00%
B	Summary (A)			675,998.40	100.00%	-	0.00%	675,998.40	100.00%	675,998.40	100.00%	-	0.00%
C	Less Advance Payment 40.00 %			-		-		-		-		-	
D	Total (B-C)			675,998.40	100.00%	-	0.00%	675,998.40	100.00%	675,998.40	100.00%	-	0.00%
E	Vat 7%			47,319.89	100.00%	-	0.00%	47,319.89	100.00%	47,319.89	100.00%	-	0.00%
F	Include Vat (D+E)			723,318.29	100.00%	-	0.00%	723,318.29	100.00%	723,318.29	100.00%	-	0.00%
and three	Retention 5% Of (E)			33,799.92	100.00%	-	0.00%	33,799.92	100.00%	33,799.92	100.00%	-	0.00%
H	Total Less Retention (F-G)			689,518.37	100.00%	-	0.00%	689,518.37	100.00%	689,518.37	100.00%	-	0.00%
I	Withholding Tax 3% Of (D)			20,279.95	100.00%	-	0.00%	20,279.95	100.00%	20,279.95	100.00%	-	0.00%
J	Net Payment (H-I)			669,238.42	100.00%	-	0.00%	669,238.42	100.00%	669,238.42	100.00%	-	0.00%


(Mr. Thanapon Wittayaphon)

Project Manager

BANGKOK DEC-CON PUBLIC COMPANY LIMITED

Date....12.....02.....2026.....

(Mr. Clarence Sim)

Project Consultant

CMP Management ASIA CO., LTD.

Date...../...../.....

PAYMENT Claim VO of Final Account SI-050

PROJECT : ATLAS SUPER CLUB
SUBJECT : INTERIOR
BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

No. BKD(QS)/QUOT/SPC/ASC/68-103/REV.04
DATE : 24/2/2026
REVISION : 4



ITEM	DESCRIPTION	QUANTITY	UNIT	AMOUNT (BAHT)	AMOUNT (BAHT)	AMOUNT (BAHT)	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value	
				CONTRACT VALUE (2)	VO VALUE (SI) (3)	VO VALUE (PENDING) (4)	CURRENT VALUE (2)+(3)+(4)=(5)								
	INTERIOR WORK							%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)
1	SEATING AREA	1	UNIT	19,575,757.00	4,476,577.50	532,280.00	24,584,614.50	0%		100%	532,280.00	2%	532,280.00	0%	0.00
2	MAIN BAR AREA	1	UNIT	4,269,365.00	(177,057.00)	455,290.00	4,547,598.00	0%		100%	455,290.00	10%	455,290.00	0%	0.00
3	LOBBY AREA + LOBBY W.C.	1	UNIT	3,757,224.00	3,127,569.25	-	6,884,793.25	0%		100%	-	0%	-	0%	0.00
4	GREETER AREA	1	UNIT	1,355,787.00	1,608,060.00	-	2,963,847.00	0%		100%	-	0%	-	0%	0.00
5	MAIN W.C. FOYER AREA	1	UNIT	701,492.00	40,057.00	56,000.00	797,549.00	0%		100%	56,000.00	7%	56,000.00	0%	0.00
6	MAIN W.C. (PUBLIC AREA)	1	UNIT	5,214,311.00	(44,469.00)	-	5,169,842.00	0%		100%	-	0%	-	0%	0.00
7	VIP 1	1	UNIT	5,843,263.00	(121,476.00)	-	5,721,787.00	0%		100%	-	0%	-	0%	0.00
8	VIP 2	1	UNIT	10,722,856.00	(885,510.00)	-	9,837,346.00	0%		100%	-	0%	-	0%	0.00
9	VIP 3	1	UNIT	7,914,741.00	(658,529.00)	-	7,256,212.00	0%		100%	-	0%	-	0%	0.00
10	3 VIP W.C.s	1	UNIT	986,858.00	917,297.00	-	1,904,155.00	0%		100%	-	0%	-	0%	0.00
11	VIP CORRIDOR AREA	1	UNIT	1,805,572.00	542,898.10	-	2,348,470.10	0%		100%	-	0%	-	0%	0.00
	PROVISIONAL SUM										-				
12	PRO-SUM TILE	1	UNIT	807,180.00			-				-				
13	PRO-SUM DECORATIVE COLUMN	1	UNIT	5,909,647.00			-				-				
14	PRO-SUM RAILING/BALUSTRADE	1	UNIT	1,103,871.00			-				-				
15	PRO-SUM ADDITIONAL SCOPE OF WORKS (SI-040)	1	UNIT				- 440,000.00	0%		100%	- 440,000.00	100%	- 440,000.00	0%	0.00
	TOTAL COST			69,967,924.00	8,825,417.85	1,043,570.00	71,576,213.85		-		603,570.00		603,570.00		-
	PRELIM	5%		3,512,100.00			3,512,100.00		-						-
	OVERHEAD	12%		8,396,150.88	1,059,050.14	125,228.40	8,589,145.66		-		72,428.40		72,428.40		-
	SUMMARY COST			81,876,174.88	9,884,467.99	1,168,798.40	83,677,459.51		-		675,998.40		675,998.40		-

BILL OF QUANTITIES

PAYMENT Claim VO of Final Account SI-050

PROJECT : ATLAS SUPER CLUB
SUBJECT : INTERIOR (WITH FRB WALL)
BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED



DESCRIPTION (VO BOQ)					VO TOTAL		VO TOTAL	VO TOTAL	Previous Claimed		Claim this month		Comalative to date		Remaining value	
ITEM	VO Ref.	PJ Ref.	CODE	DESCRIPTION (VE BOQ)	TOTAL (3) DIFF (SI)	TOTAL AMOUNT (PD)	TOTAL (4) DIFF (PD)	(3)+(4)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)
1				SEATING AREA	4,476,577.50		532,280.00	5,008,857.50	0%		100%	5,008,857.50	100%	5,008,857.50	0%	0.00
2				MAIN BAR AREA	(177,057.00)		455,290.00	278,233.00	0%		100%	278,233.00	100%	278,233.00	0%	0.00
3				LOBBY AREA + LOBBY W.C.	3,127,569.25		-	3,127,569.25	0%		100%	3,127,569.25	100%	3,127,569.25	0%	0.00
4				GREETER AREA	1,608,060.00		-	1,608,060.00	0%		100%	1,608,060.00	100%	1,608,060.00	0%	0.00
5				MAIN W.C. FOYER AREA	40,057.00		56,000.00	96,057.00	0%		100%	96,057.00	100%	96,057.00	0%	0.00
6				MAIN W.C. (PUBLIC AREA)	(44,469.00)		-	(44,469.00)	0%		100%	(44,469.00)	100%	(44,469.00)	0%	0.00
7				VIP 1	(121,476.00)		-	(121,476.00)	0%		100%	(121,476.00)	100%	(121,476.00)	0%	0.00
8				VIP 2	(885,510.00)		-	(885,510.00)	0%		100%	(885,510.00)	100%	(885,510.00)	0%	0.00
9				VIP 3	(658,529.00)		-	(658,529.00)	0%		100%	(658,529.00)	100%	(658,529.00)	0%	0.00
10				3 VIP W.C.s	917,297.00		-	917,297.00	0%		100%	917,297.00	100%	917,297.00	0%	0.00
11				VIP CORRIDOR AREA	542,898.10		-	542,898.10	0%		100%	542,898.10	100%	542,898.10	0%	0.00
1				SEATING AREA												
				FLOOR												
1.4.1	RVO.065	SPC-VO-065		GAP SEALING WITH POLYURETHANE FOAM FOR ALL SOFA GAPS		-	-	-								
1.4.2	RVO.065	SPC-VO-065		CAST THE GROOVE WITH SELF-LEVELING CEMENT FOR ALL SOFA GAPS		-	-	-								
1.4.3	RVO.071	SPC-VO-071		CANTILEVER STAGE, VINYL (ANTI-SLIP) Biotite 4203 NCS S8000-N By Polyflor 2.5 mm.		15,080.00	15,080.00	15,080.00	0%		100%	15,080.00	100%	15,080.00	0%	0.00
1.4.4	RVO.071	SPC-VO-071		MAIN STAGE, WALL EDGE COVERING FOR AVL SYSTEM WITH PRO-WALL STRUCTURE HMR BACKING PAINTED WITH PA-02 BLACK PAINT		15,280.00	15,280.00	15,280.00	0%		100%	15,280.00	100%	15,280.00	0%	0.00
				STAIRS FINISHING+HANDRAIL												
1.7.1	RVO.070	SPC-VO-070		ADDITIONAL BALUSTRADE, TITANIUM PAINTED STEEL MT-01A WITH HARD WOODEN HANDRAIL FINISHED WITH PA-02 BLACK PAINT		144,130.00	144,130.00	144,130.00	0%		100%	144,130.00	100%	144,130.00	0%	0.00
				BUILT-IN FURNITURE												
1.30	RVO.064	SPC-VO-064	BF-37	FOH COUNTER, STEEL STRUCTURE HMR BACKING WITH PA-02 BLACK SPRAY PAINT AND SP-02 BLACK TEXTURE PAINT FINISH EXCL. CLEAR ACRYLIC 5 MM. FOR PARTITION 3 M.		303,570.00	303,570.00	303,570.00	0%		100%	303,570.00	100%	303,570.00	0%	0.00
				DOOR												
1.31.1	RVO.069	SPC-VO-069	D11	COWBOY DOOR, FINISHED WITH PA-02 BLACK PAINT INCL. DOOR HARDWARE		-	-	-								
1.31.2	RVO.069	SPC-VO-069	D13	SINGLE DOOR DIM. 1.0X2.45 M. FINISHED WITH PA-02 BLACK PAINT INCLUDING DOOR HARDWARE		54,220.00	54,220.00	54,220.00	0%		100%	54,220.00	100%	54,220.00	0%	0.00

BILL OF QUANTITIES

PAYMENT Claim VO of Final Account SI-050

PROJECT : ATLAS SUPER CLUB
SUBJECT : INTERIOR (WITH FRB WALL)
BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED



DESCRIPTION (VO BOQ)					VO TOTAL		VO TOTAL	VO TOTAL	Previous Claimed		Claim this month		Comalative to date		Remaining value	
ITEM	VO Ref.	PJ Ref.	CODE	DESCRIPTION (VE BOQ)	TOTAL (3) DIFF (SI)	TOTAL AMOUNT (PD)	TOTAL (4) DIFF (PD)	(3)+(4)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)
1.31.3	RVO.069	SPC-VO-069	D14	SINGLE DOOR FINISHED WITH SP-02 TEXTURE BLACK PAINT INCL. DOOR HARDWARE		-	-	-								
2			MAIN BAR AREA													
				FLOOR												
2.1.3	RVO.064	SPC-VO-064		SELF-LEVELING WITH BACKING VIVA BOARD 15+15 MM. AT CAROUSEL AREA		90,150.00	90,150.00	90,150.00	0%		100%	90,150.00	100%	90,150.00	0%	0.00
				CEILING												
2.2.1	RVO.066	SPC-VO-066		ADDITIONAL SCAFFOLDING FOR CAROUSEL AREA		-	-	-								
				BUILT-IN FURNITURE												
2.4.1	RVO.064	SPC-VO-064	BF-14	CURVED SOFA IN CAROUSEL AREA, CURVED SOFA SEATING, WOODEN STRUCTURE HMR BACKING FINIHED SP-04 TITANIUM SPRAY, FABRIC BY OWNER EXCL. LED STRIP LIGHT		209,420.00	209,420.00	209,420.00	0%		100%	209,420.00	100%	209,420.00	0%	0.00
2.4.2	RVO.064	SPC-VO-064	BF-14.1	CURVED TOP BAR, STEEL STRUCTURE HMR BACKING FINISHED WITH SP-04 TITANIUM SPRAY		56,640.00	56,640.00	56,640.00	0%		100%	56,640.00	100%	56,640.00	0%	0.00
2.4.3	RVO.064	SPC-VO-064	BF-03	FIXED TABLE, ST-04 BLUE TILE TOP YS321, HIGH GLOSS SURFACE THK. 9 MM. 75x150 CM. AND STEEL BODY FINISHED MT-01A TITANIUM SPRAY PAINT.		60,480.00	60,480.00	60,480.00	0%		100%	60,480.00	100%	60,480.00	0%	0.00
				DOOR												
2.5.2	RVO.069	SPC-VO-069	D12	COWBOY DOOR, FINISHED WITH PA-02 BLACK PAINT AND SP-04 TITANIUM SPRAY PAINT INCL. DOOR HARDWARE		11,490.00	11,490.00	11,490.00	0%		100%	11,490.00	100%	11,490.00	0%	0.00
2.5.3	RVO.069	SPC-VO-069	D13	SINGLE DOOR DIM. 1.0X2.45 M. FINISHED WITH PA-02 BLACK PAINT INCLUDING DOOR HARDWARE		27,110.00	27,110.00	27,110.00	0%		100%	27,110.00	100%	27,110.00	0%	0.00
5			MAIN W.C. FOYER AREA													
				WALL												
5.6.1	RVO.068	SPC-VO-068		TOILET SIGNAGE, ZINC FINISHED WITH GLOSSY BLACK AND WHITE ACRYLIC INCLUDING WARM WHITE LIGHTING FOR TOILET SYMBOLS		56,000.00	56,000.00	56,000.00	0%		100%	56,000.00	100%	56,000.00	0%	0.00

SECTION

1. S-Curve




PROJECT : ATLAS SUPERCLUB

OWNER : HW Group / Ratchada Entertainment

CONSULTANT : CMP Management Asia Co.,Ltd.

CONTRACTOR : Bangkok Dec-Con Public Company Limited

VO. progress S-curve

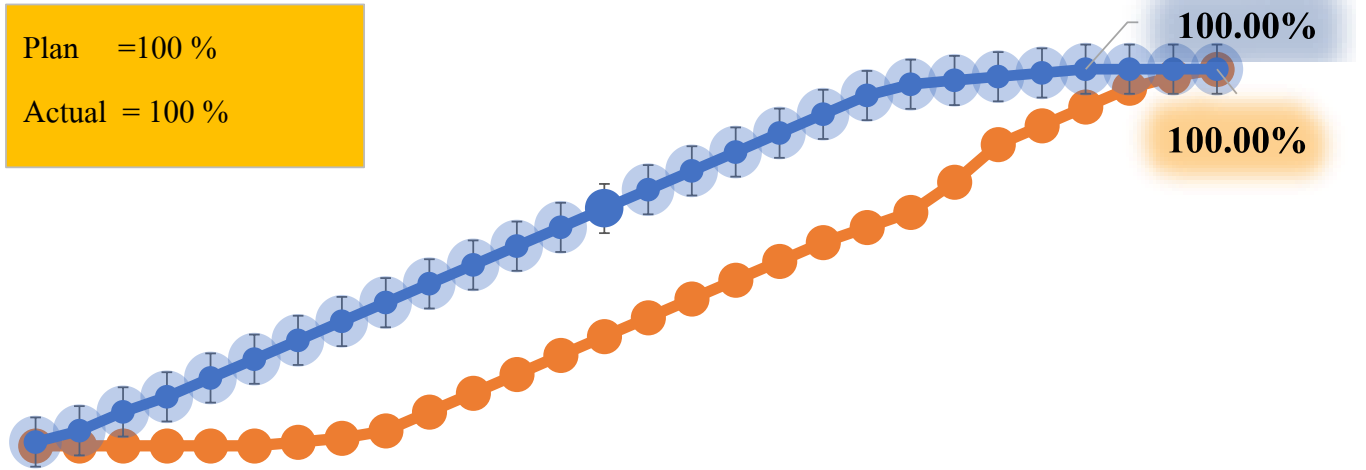

SECTION

2. Advancement Photos



PROJECT : ATLAS SUPERCLUB

OWNER : HW Group / Ratchada Entertainment

CONSULTANT : CMP Management Asia Co.,Ltd.

CONTRACTOR : Bangkok Dec-Con Public Company Limited




Photos of Completed Work






Photos of Completed Work

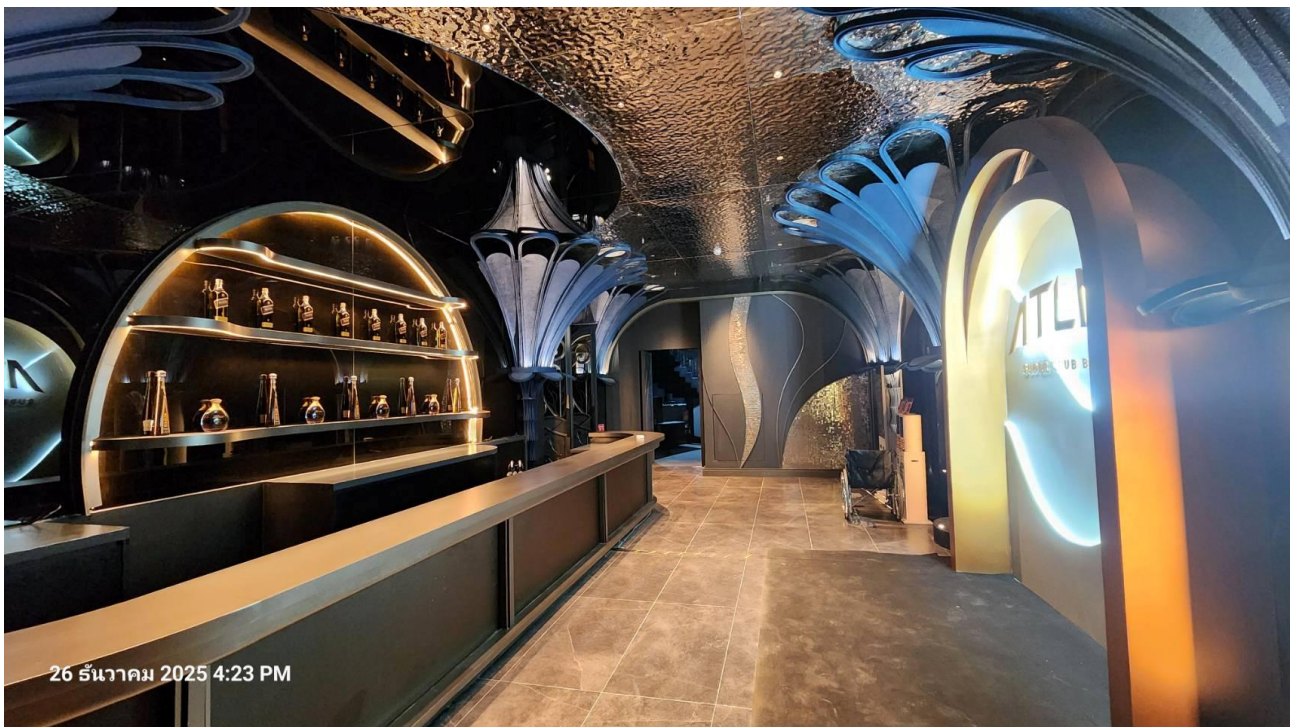





Photos of Completed Work

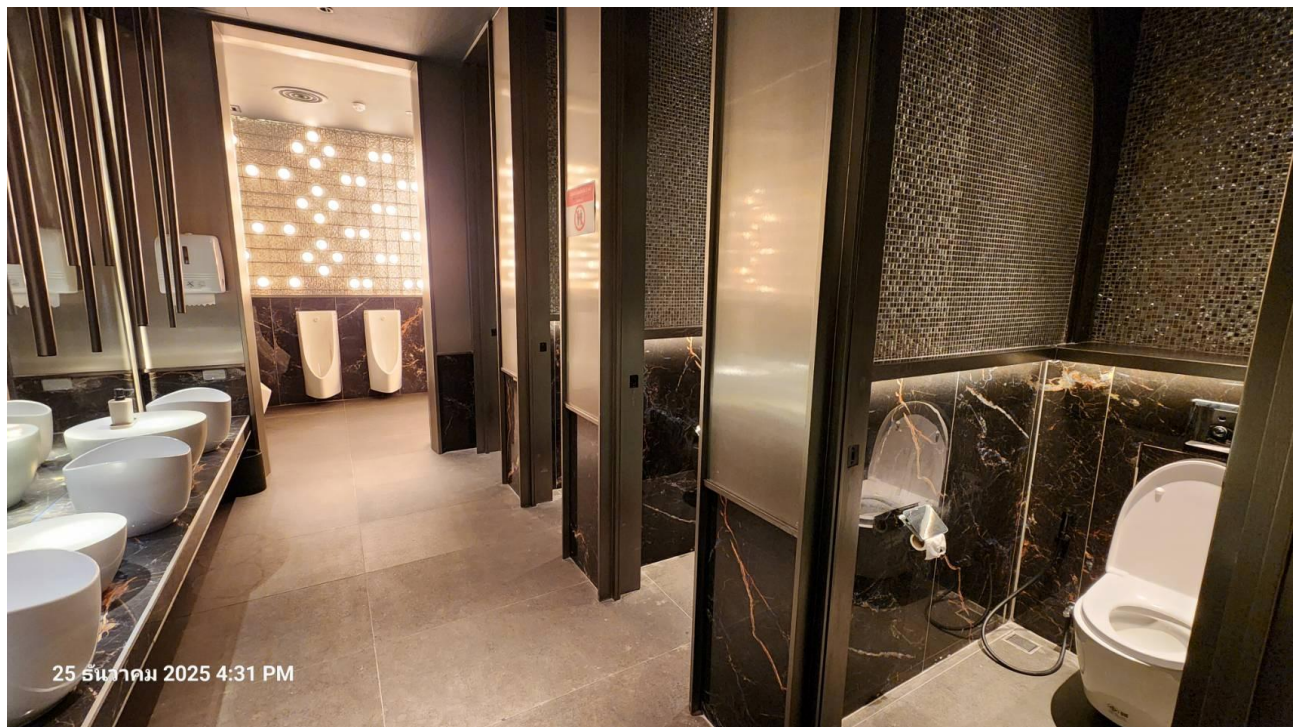



Photos of Completed Work

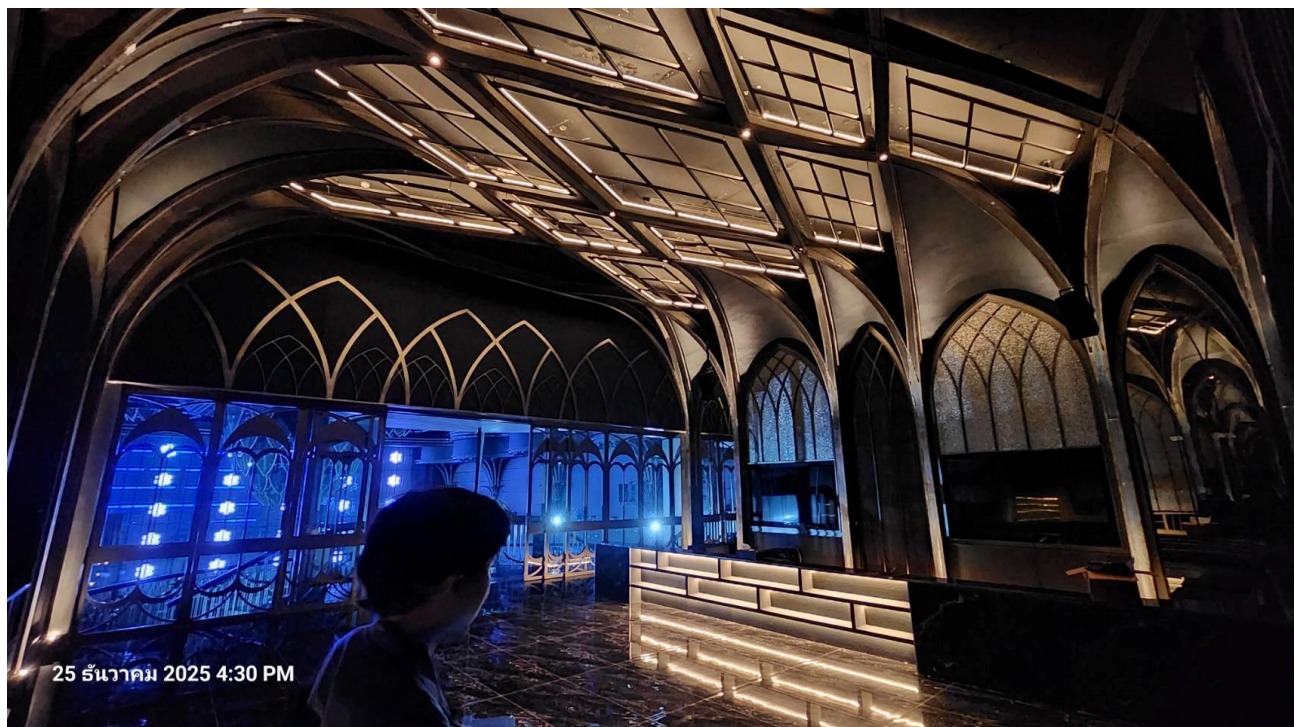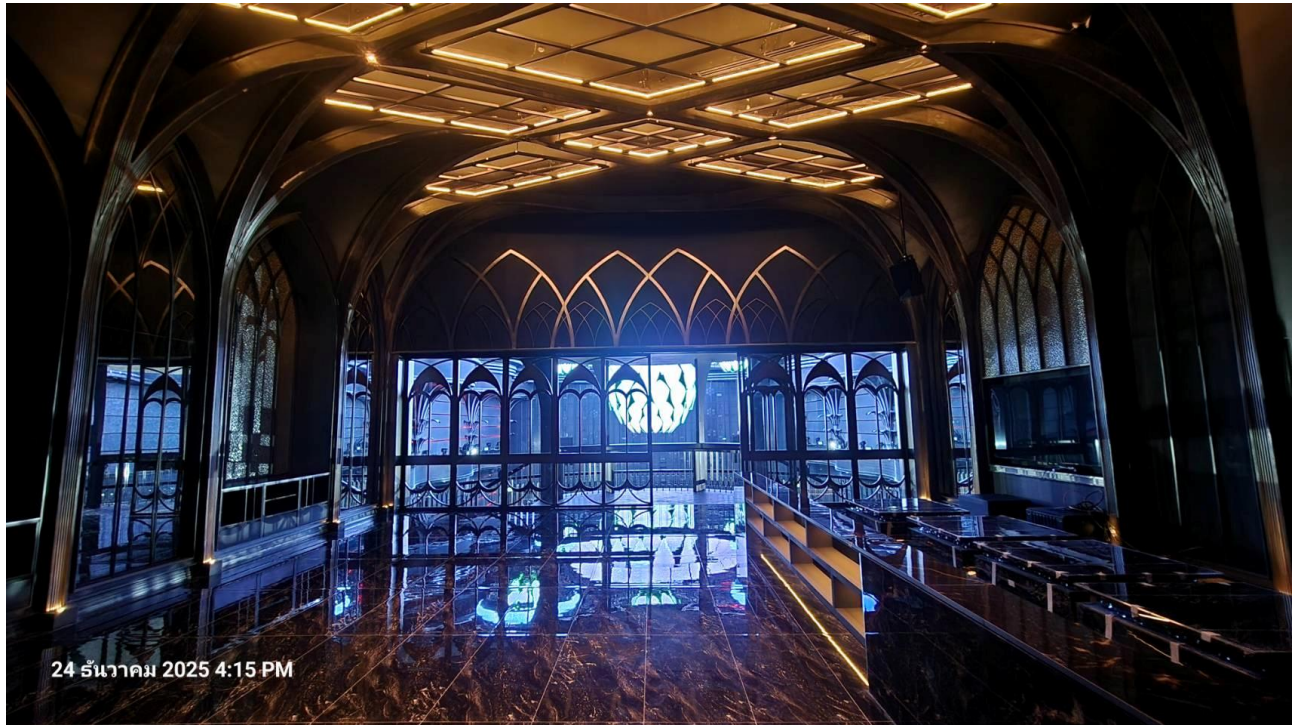




Photos of Completed Work





Photos of Completed Work

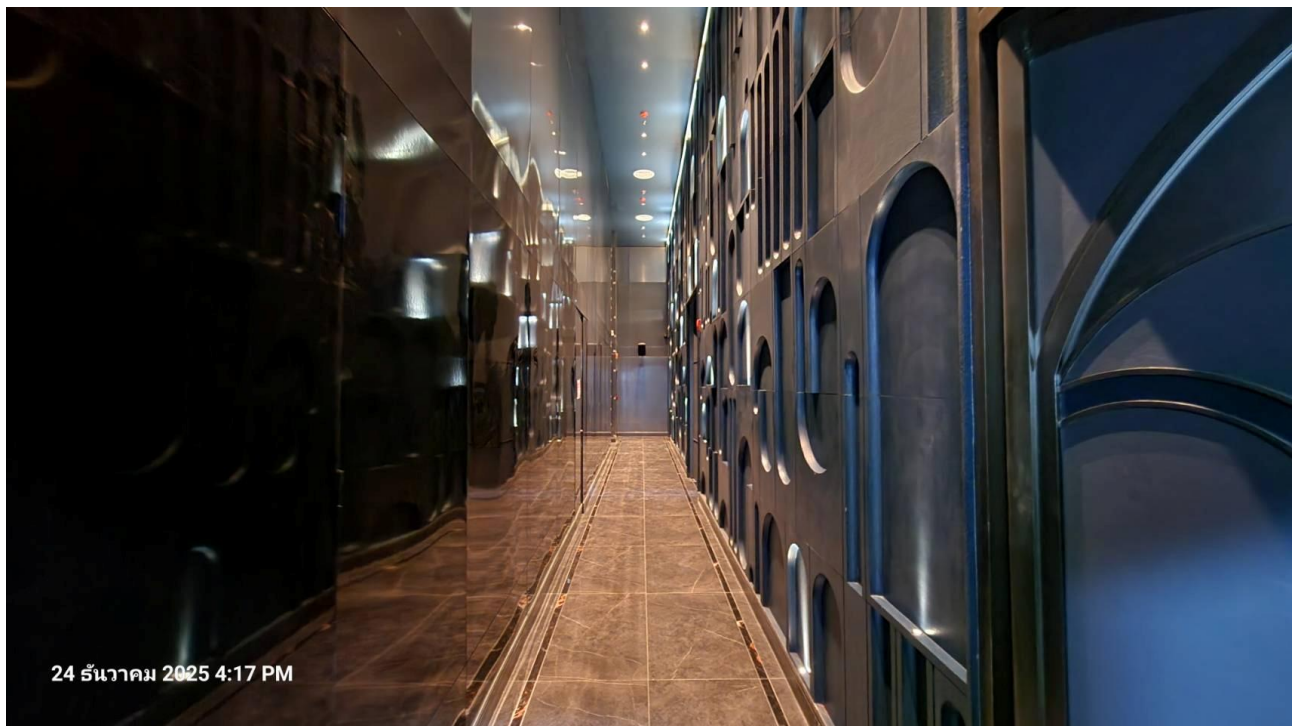



Photos of Completed Work

