ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED

034/132-161 ITAL-THAI TOWER BLDG., NEW PETCHBURI RD., KWAENG BANGKAPI,

KHET HUAYKWANG, BANGKOK (HEAD OFFICE TAX.ID. 0107537000939)

J.2596 Atlas Super Club Ratchada Project

No. 25962025/018

29 January 2026

# INVOICE

Customer Ratchada Entertainment Group Co., Ltd. TAX ID. 0105566107710

Address 58 Ratchadaphisek Road, Soi 4, Huaykhwang Subdistrict,

Huaykhwang District, Bangkok, Thailand 10310

| No. | Description | Amount |
|---|---|---|
| 1 | Interim Payment No.018 of Atlas Super Club Ratchada Project | 114,863.49 |
| | Refer Letter No. 1.0/ITD/ASC/PAYMENT/018 | |
| | Less Retention 5% | - |
| | Total | 114,863.49 |
| | VAT 7% | 8,040.44 |
| | Total Payment (Include VAT) | 122,903.93 |
| | Less Withholding Tax 3% | (3,445.90) |
| | Net Payment | 119,458.03 |

One Hundred Nineteen Thousand Four Hundred Fifty Eight Baht and Three Satang

Authorized Signature .....

(Mr.Danai Suwanmanee)

Project Engineer

# REQUEST FOR APPROVAL (Payment)

CMP MANAGEMENT ASIA Co.,Ltd.

Italian-Thai Development Public Limited Company

Project : Atlas Superclub Ratchada

Ref : NO. 1.0/ITD/ASC/Payment/017

Date 29 January 2026

Subject : Interim Payment

Description : Payment No.18

Type Of Work : No. 25962025/018

Attached : ☑ 1) Letter 2) Summary payment No.17

3) LOA

Others :

Remark :

---

Attn : CMP Management Asia Co., Ltd. (CMP)

☐ For Designer Opinion ☑ For Approval

☐ For Information ☐ See notes

Notes

From : Italian-Thai Development Public Limited Company

Signature :

(Mr Danai Suwwanmanee)

Project Manager

Date : Time :

.

---

Attn : Owner/Designer……..

☐ For comment ☐ For Approval

☐ For Information ☐ See notes

Notes

From : CMP Management Asia Co., Ltd.

Signature :

( )

Project Manager / CMP

Date : Time :

---

Attn : CMP Management Asia Co., Ltd.

☐ Approval ☐ Approval As Noted

☐ Resubmit ☐ Not Approved

Notes

From : Owner/Designer

Signature :

( )

Project Manager / Designer

Date : Time :

---

Attn : Italian Thai Development Public Limit Company

☐ Approval ☐ Approval As Noted

☐ Resubmit ☐ Not Approved

Notes

:

From : CMP Management Asia Co., Ltd.

Signature :

( )

Project Manager / CMP

Date : Time :

---

cc. ☐ Original(ITD) ☐ HWG ☐ CMP ☐ Designer

Registration No. 0107537000939

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**

29 January 2026

NO. 1.0/ITD/ASC/Payment/018

Subject Payment No.18
ATLAS SUPERCLUB

Attn Mr. Clarence Sim
CMP Management Asia Co., Ltd.

Reference LOA : Letter of Agreement 26 April 2024

Attachment
1) BOQ Breakdown Work Done
2) Drawing Mark Up Work Done
3) Photo Show Work Done

We, Italian-thai Development Public Company Ltd. that has been entrusted to perform the main construction works, would like to request payment No.18 of 119,458.03 Baht (One Hundred Nineteen Thousand Four Hundred Fifty Eight Baht and Three Satang) Net Paymant, details as per the attached documents.

Your approval would be appreciated.

Sincerely Yours,

(Mr. Danai Suwanmanee)
Project Engineer
Italian-Thai Devevelopment Pcl.

**Project**

**Atlas Superclub Ratchada.**

**Location : 58 Ratchadaphisek Road, Soi 4, Huai Khwang Subdistrict, Huai Khwang , Bangkok 10310**

**Owner: HW Group / Ratchada Entertainment**

# PROGRESS CLAIM NO.18 FOR APPROVE

**Period 1 December 2025 - 31 December 2025**

**Reference LOA : Letter of Agreement 26 April 2024**

**BY**


**Italain-Thai Development Public Limited**

**2034/132-161ITALTAHITOWER,**

**NEWPETCHBURIROAD,BANGKAPI, HUAYKWANG,BANGKOK10310, THAILAND**

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB RATCHADA.**
**SUMMARY OF PAYMENT CLAIM**

Payment Claim No.18
January 29, 2026

| Item | Description | Unit | Contract | | | Previous ITD | | This month ITD | | Cumulative to current period ITD | | Balances | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | QTY. | ITD | % | Total | % | Total | % | Total | % | Total | % |
| | **Summary of construction costs of the project.** | | | | | | | | | | | | |
| A | Structural Works (After contract adjustment) | LS | 1 | 26,430,260.40 | 100.00% | 26,430,260.40 | 100.00% | - | 0.00% | 26,430,260.40 | 100.00% | - | 0.00% |
| B | Architectural Works | LS | 1 | 16,791,095.33 | 100.00% | 16,686,673.96 | 99.38% | 104,421.37 | 0.62% | 16,791,095.33 | 100.00% | - | 0.00% |
| C | Preliminary Cost | LS | 1 | 4,755,448.70 | 100.00% | 4,755,448.70 | 100.00% | | 0.00% | 4,755,448.70 | 100.00% | - | 0.00% |
| D | Overhead and Profit | | 1 | 4,322,135.57 | 100.00% | 4,311,693.45 | 99.76% | 10,442.12 | 0.24% | 4,322,135.57 | 100.00% | - | 0.00% |
| **E** | **Summary ( A+B+C+D )** | | | **52,298,940.00** | **100.00%** | **52,184,076.51** | **99.78%** | **114,863.49** | **0.22%** | **52,298,940.00** | **100.00%** | **-** | **0.00%** |
| | | | | LS | | | | | | | | | |
| F | Advance Payment ltd 10% | | | - | | - | | - | | - | | - | |
| G | Less Advance Payment ltd | | | - | | - | | - | | - | | - | |
| **H** | **Total ( E+F+G )** | | | **52,298,940.00** | **100.00%** | **52,184,076.51** | **99.78%** | **114,863.49** | **0.22%** | **52,298,940.00** | **100.00%** | **-** | **0.00%** |
| I | Vat 7% | | | 3,660,925.80 | 100.00% | 3,652,885.36 | 99.78% | 8,040.44 | 0.22% | 3,660,925.80 | 100.00% | - | 0.00% |
| **J** | **Include Vat ( H+I )** | | | **55,959,865.80** | **100.00%** | **55,836,961.87** | **99.78%** | **122,903.93** | **0.22%** | **55,959,865.80** | **100.00%** | **-** | **0.00%** |
| K | Retention 5% Of ( E ) | | | 2,614,947.00 | | 2,614,947.00 | | - | | 2,614,947.00 | | - | |
| **L** | **Total Less Retention ( J+K )** | | | **53,344,918.80** | | **53,222,014.87** | | **122,903.93** | | **53,344,918.80** | | **-** | |
| M | Withholding Tax 3% Of ( H ) | | | 1,568,968.20 | | 1,565,522.30 | | 3,445.90 | | 1,568,968.20 | | - | |
| **N** | **Net Payment ( L+M )** | | | **51,775,950.60** | | **51,656,492.57** | | **119,458.03** | | **51,775,950.60** | | **-** | |

Please consider

(.....)
Mr.Danai Suwanmanee
Project Engineer
ITALIAN-THAI

Consider approve

(.....)
Mr.Clarence Sim
Project Director
CMP Management Asia

**Bill Of Quantities**

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB RATCHADA.**
**SUMMARY OF BILL QUANTITIES**

| Item | Description | Unit | Qty. | Total Amount | Previous Accumlate | | Work in This Period | | Accumulate This Period | | Remaining Work | | Remark |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | % | Amount (Baht) | % | Amount (Baht) | % | Amount (Baht) | % | Amount (Baht) | |
| | | | | | | | | | | | | | |
| A | Structural Works | LS. | 1.00 | 29,794,860.40 | 100.00% | 29,794,860.40 | 0.00% | - | 100.00% | 29,794,860.40 | 0.00% | - | |
| A.1 | Deduction Piling Work | LS. | 1.00 | (3,364,600.00) | 100.00% | (3,364,600.00) | 0.00% | - | 100.00% | (3,364,600.00) | 0.00% | - | |
| B | Architectural Works | LS. | 1.00 | 16,791,095.33 | 99.38% | 16,686,673.96 | 0.62% | 104,421.37 | 100.00% | 16,791,095.33 | 0.00% | - | |
| | | | | | | | | | | | | | |
| **C** | **Sub Total** | | | **43,221,355.73** | **99.76%** | **43,116,934.36** | **0.24%** | **104,421.37** | **100.00%** | **43,221,355.73** | **0.00%** | **-** | **-** |
| | | | | | | | | | | | | | |
| D | Preliminary Cost | | | 4,755,448.70 | 100.00% | 4,755,448.70 | 0.00% | - | 100.00% | 4,755,448.70 | 0.00% | - | |
| E | Overhead and Profit | | | 4,322,135.57 | 99.76% | 4,311,693.45 | 0.24% | 10,442.12 | 100.00% | 4,322,135.57 | 0.00% | - | |
| | | | | | | | | | | | | | |
| **F** | **Total (Excl. Vat. 7%)** | | | **52,298,940.00** | **99.78%** | **52,184,076.51** | **0.22%** | **114,863.49** | **100.00%** | **52,298,940.00** | **0.00%** | **-** | |
| | | | | | | | | | | | | | |
| G | Vat.7% | | | 3,660,925.80 | 99.78% | 3,652,885.36 | 0.22% | 8,040.44 | 100.00% | 3,660,925.80 | 0.00% | - | |
| | | | | | | | | | | | | | |
| **H** | **Total (Incl. Vat. 7%)** | | | **55,959,865.80** | **99.78%** | **55,836,961.87** | **0.22%** | **122,903.93** | **100.00%** | **55,959,865.80** | **0.00%** | **-** | |

**Bill Of Quantities**

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB RATCHADA.**
**ARCHITECTURAL WORKS**

| Item | Description | Unit | Qty. | Total Amount | Previous Accumlate | | | Work in This Period | | | Accumulate This Period | | | Remaining Work | | | Remark |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | |
| | | | | | | | | | | | | | | | | | |
| | **ARCHITECTURAL WORKS** | | | | | | | | | | | | | | | | |
| 1 | Roof Finishes | LS. | 1.00 | 1,901,158.00 | - | 100.00% | 1,901,158.00 | - | 0.00% | - | - | 100.00% | 1,901,158.00 | - | 0.00% | - | |
| 2 | Floor Finishes | LS. | 1.00 | 1,854,970.00 | - | 100.00% | 1,854,970.00 | - | 0.00% | - | - | 100.00% | 1,854,970.00 | - | 0.00% | - | |
| 3 | Wall & Wall Finishes | LS. | 1.00 | 8,263,927.00 | - | 100.00% | 8,263,927.00 | - | 0.00% | - | - | 100.00% | 8,263,927.00 | - | 0.00% | - | |
| 4 | Ceiling | LS. | 1.00 | 1,805,400.00 | - | 100.00% | 1,805,400.00 | - | 0.00% | - | - | 100.00% | 1,805,400.00 | - | 0.00% | - | |
| 5 | Painting Finishes | LS. | 1.00 | 730,350.00 | - | 100.00% | 730,350.00 | - | 0.00% | - | - | 100.00% | 730,350.00 | - | 0.00% | - | |
| 6 | Sanitary Fixtures | LS. | 1.00 | 507,821.00 | - | 100.00% | 507,821.00 | - | 0.00% | - | - | 100.00% | 507,821.00 | - | 0.00% | - | |
| 7 | Door | LS. | 1.00 | 1,044,213.73 | - | 90.00% | 939,792.36 | - | 10.00% | 104,421.37 | - | 100.00% | 1,044,213.73 | - | 0.00% | - | |
| 8 | Stair | LS. | 1.00 | 318,077.60 | - | 100.00% | 318,077.60 | - | 0.00% | - | - | 100.00% | 318,077.60 | - | 0.00% | - | |
| 9 | Additional Work | LS. | 1.00 | 365,178.00 | - | 100.00% | 365,178.00 | - | 0.00% | - | - | 100.00% | 365,178.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Total Architectural Works** | | | **16,791,095.33** | | **99.38%** | **16,686,673.96** | | **0.62%** | **104,421.37** | | **100.00%** | **16,791,095.33** | | **0.00%** | **-** | |

**Bill Of Quantities**

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB RATCHADA.**
**ARCHITECTURAL WORKS**

| Item | Description | Unit | Qty. | Total Amount | Previous Accumlate | | | Work in This Period | | | Accumulate This Period | | | Remaining Work | | | Remark |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | |
| | | | | | | | | | | | | | | | | | |
| **1** | **Roof Finishes and Siding** | | | | | | | | | | | | | | | | |
| 1.1 | Metal Sheet/w PU Foam 2" Insulation | sq.m | 1,276.00 | 1,031,008.00 | - | 100.00% | 1,031,008.00 | - | 0.00% | - | - | 100.00% | 1,031,008.00 | - | 0.00% | - | |
| 1.2 | Roof gutter SUS304 Thk.=0.50mm. | m. | 105.00 | 843,150.00 | - | 100.00% | 843,150.00 | - | 0.00% | - | | 100.00% | 843,150.00 | - | 0.00% | - | |
| 1.3 | Roof Drain 4" | nos. | 18.00 | 27,000.00 | - | 100.00% | 27,000.00 | - | 0.00% | - | - | 100.00% | 27,000.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 1 : Roof Finishes** | | | **1,901,158.00** | | **100.00%** | **1,901,158.00** | | **0.00%** | **-** | | **100.00%** | **1,901,158.00** | | **0.00%** | **-** | |
| **2** | **Floor Finishes** | | | | | | | | | | | | | | | | |
| 2.1 | F1 - Floors on the 1st-3rd floors, tiled at 2 right angles per room | sq.m | 389.00 | 369,550.00 | - | 100.00% | 369,550.00 | - | 0.00% | - | - | 100.00% | 369,550.00 | - | 0.00% | - | |
| 2.2 | F2 - Hall floors, walkways, and various hall areas are laid with tiles at right angles, 2 patterns per room. | sq.m | 901.00 | 855,950.00 | - | 100.00% | 855,950.00 | - | 0.00% | - | - | 100.00% | 855,950.00 | - | 0.00% | - | |
| 2.3 | F3 - Bathroom floor, balcony with 2 right corner tiles per room | sq.m | 38.00 | 27,360.00 | - | 100.00% | 27,360.00 | - | 0.00% | - | - | 100.00% | 27,360.00 | - | 0.00% | - | |
| 2.4 | F4 - Parking Area, Road Level Rough polished concrete floors | sq.m | | | | | | | | - | | | | | | | |
| 2.5 | F6 - Entrance hall floor, tiled at right angles, 2 patterns per room | sq.m | 195.00 | 39,000.00 | - | 100.00% | 39,000.00 | - | 0.00% | - | - | 100.00% | 39,000.00 | - | 0.00% | - | |
| 2.6 | F7 - main staircase floor. Granite paving at right angles 2 patterns per room | sq.m | 45.00 | 123,750.00 | - | 100.00% | 123,750.00 | - | 0.00% | - | - | 100.00% | 123,750.00 | - | 0.00% | - | |
| 2.5 | F5 - Deck Floor, Awning The skin is polished and smooth | sq.m | | | | | | | | | | | | | | | |
| Add.3 | Cement and sand for leveling | sq.m | 1,373.00 | 274,600.00 | - | 100.00% | 274,600.00 | - | 0.00% | - | - | 100.00% | 274,600.00 | - | 0.00% | - | |
| Add.4 | Adhesive cement and grout | sq.m | 1,373.00 | 164,760.00 | - | 100.00% | 164,760.00 | - | 0.00% | - | - | 100.00% | 164,760.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 2 : Floor Finishes** | | | **1,854,970.00** | | **100.00%** | **1,854,970.00** | | **0.00%** | **-** | | **100.00%** | **1,854,970.00** | | **0.00%** | **-** | |
| **3** | **Wall & Wall Finishes** | | | | | | | | | | | | | | | | |
| **3** | **Wall** | | | | | | | | | | | | | | | | |
| 3.1 | Wall Aerated Brick Q-CON with 10 cm Thick Plaster (Wall Tile) | sq.m | 769.00 | 689,793.00 | - | 100.00% | 689,793.00 | - | 0.00% | - | - | 100.00% | 689,793.00 | - | 0.00% | - | |
| 3.2 | Wall Aerated Brick Q-CON with 10 cm thick plaster (general room wall) | sq.m | 1,744.00 | 1,564,368.00 | - | 100.00% | 1,564,368.00 | - | 0.00% | - | - | 100.00% | 1,564,368.00 | - | 0.00% | - | |
| 3.3 | Decorative walls, fireproof walls 50 cm thick | sq.m | 2,912.00 | 5,387,200.00 | - | 100.00% | 5,387,200.00 | - | 0.00% | - | - | 100.00% | 5,387,200.00 | - | 0.00% | - | |
| 3.4 | Skim ผนังภายนอกอาคาร | sq.m | 2,912.00 | 384,384.00 | - | 100.00% | 384,384.00 | - | 0.00% | - | - | 100.00% | 384,384.00 | - | 0.00% | - | |
| | **Wall Finish** | | | | | | | | | | | | | | | | |
| 3.5 | P1 - External walls, smooth plaster. | sq.m | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 3.6 | P2 - Internal walls, smooth plaster. | sq.m | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 3.7 | P3 - Rough plastering, tiling, floor-to-ceiling | sq.m | 91.00 | 67,340.00 | - | 100.00% | 67,340.00 | - | 0.00% | - | - | 100.00% | 67,340.00 | - | 0.00% | - | |
| 3.8 | P4 - Decorative walls, fireproof walls, 15 cm thick | sq.m | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 3.9 | P5 - Rough plaster | sq.m | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 3.10 | P7 - Skim coat concrete wall | sq.m | 97.85 | 11,742.00 | - | 100.00% | 11,742.00 | - | 0.00% | - | - | 100.00% | 11,742.00 | - | 0.00% | - | |
| 3.11 | P8 - Rough plastering, tiling, floor-to-ceiling | sq.m | 215.00 | 159,100.00 | - | 100.00% | 159,100.00 | - | 0.00% | - | - | 100.00% | 159,100.00 | - | 0.00% | - | |
| 3.12 | P9 - Decorative Walls, Acoustic Acoustic Boards, Sound Absorbers | sq.m | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 3.13 | P10 - Decorative walls, fireproof walls Steel beard frame Cover with wooden slats. Identify materials from designers later | sq.m | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 3.14 | P11 - Decorative walls, 5 decorative walls, steel frame Cover the surface with aluminum composite sheet according to the specified design | sq.m | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 3 : Wall & Wall Finishes** | | | **8,263,927.00** | | **100.00%** | **8,263,927.00** | | **0.00%** | **-** | | **100.00%** | **8,263,927.00** | | **0.00%** | **-** | |
| **4** | **Ceiling** | | | | | | | | | | | | | | | | |
| 4.1 | C1 - General interior ceiling, gypsum board ceiling, 9 mm thick, smooth plaster | sq.m | 700.00 | 385,000.00 | - | 100.00% | 385,000.00 | - | 0.00% | - | - | 100.00% | 385,000.00 | - | 0.00% | - | |
| 4.2 | C2 - Ceiling in the bathroom Gypsum board ceiling damp proof type 9 mm thick smooth plaster | sq.m | 188.00 | 112,800.00 | - | 100.00% | 112,800.00 | - | 0.00% | - | - | 100.00% | 112,800.00 | - | 0.00% | - | |

**Bill Of Quantities**

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB RATCHADA.**
**ARCHITECTURAL WORKS**

| Item | Description | Unit | Qty. | Total Amount | Previous Accumlate | | | Work in This Period | | | Accumulate This Period | | | Remaining Work | | | Remark |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | |
| 4.3 | C3 - Exterior ceiling (eaves) Gypsum board ceiling damp proof type 9 mm thick smooth plaster Galvanized Steel Beard Frame No.24 | sq.m | - | - | | | | | | | | | | | | | |
| 4.4 | C4 - Exterior fog (floor of the floor, CSL), floor of the CSL. Smooth plaster Water-based acrylic paint. | sq.m | - | - | | | | | | | | | | | | | |
| 4.5 | C5 - READY-MADE SERVICE CHANNEL Elephant Brand, size 0.45x0.45 m. (1 point for the bathroom, 4 points for the outside of each floor, location later) | SET | 14.00 | 17,500.00 | - | 100.00% | 17,500.00 | - | 0.00% | - | - | 100.00% | 17,500.00 | - | 0.00% | - | |
| 4.6 | C6 - Prefabricated floor belly, floor groove | sq.m | 94.00 | 14,100.00 | - | 100.00% | 14,100.00 | - | 0.00% | - | - | 100.00% | 14,100.00 | - | 0.00% | - | |
| 4.7 | C7 - Decorative Ceiling Hidden Plasterboard LED Plasterboard Lamp 9 mm Thickness Smooth Plaster Galvanized Steel Beard Frame No.24 | sq.m | - | - | | | | | | | | | | | | | |
| 4.8 | Insulation Ceiling with "Metal Sheet/w PU Foam 2" Insulation" | sq.m | 1,276.00 | 1,276,000.00 | - | 100.00% | 1,276,000.00 | - | 0.00% | - | - | 100.00% | 1,276,000.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 4 : Ceiling** | | | **1,805,400.00** | | **100.00%** | **1,805,400.00** | | **0.00%** | **-** | | **100.00%** | **1,805,400.00** | | **0.00%** | **-** | |
| **5** | **Painting Finishes** | | | | | | | | | | | | | | | | |
| 5.1 | Interior wall paint TOA SUPERSHIELD | sq.m | 558.00 | 83,700.00 | - | 100.00% | 83,700.00 | - | 0.00% | - | - | 100.00% | 83,700.00 | - | 0.00% | - | |
| 5.2 | Exterior wall paint TOA SUPERSHIELD | sq.m | 2,912.00 | 436,800.00 | - | 100.00% | 436,800.00 | - | 0.00% | - | - | 100.00% | 436,800.00 | - | 0.00% | - | |
| 5.3 | Interior ceiling paint TOA SUPERSHIELD (C1,C2,C5,) | sq.m | 123.00 | 18,450.00 | - | 100.00% | 18,450.00 | - | 0.00% | - | - | 100.00% | 18,450.00 | - | 0.00% | - | |
| 5.4 | Interior ceiling paint TOA SUPERSHIELD (C8) | sq.m | 1,276.00 | 191,400.00 | - | 100.00% | 191,400.00 | - | 0.00% | - | - | 100.00% | 191,400.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 5 : Painting Finishes** | | | **730,350.00** | | **100.00%** | **730,350.00** | | **0.00%** | **-** | | **100.00%** | **730,350.00** | | **0.00%** | **-** | |
| **6** | **Sanitary Fixtures** | | | | | | | | | | | | | | | | |
| 6.1 | Under Counter Basin | ชุด | 14.00 | 80,500.00 | 14.00 | 100.00% | 80,500.00 | - | 0.00% | - | - | 100.00% | 80,500.00 | - | 0.00% | 0.00 | |
| 6.2 | Water Closet | ชุด | 21.00 | 58,065.00 | 21.00 | 100.00% | 58,065.00 | - | 0.00% | - | - | 100.00% | 58,065.00 | - | 0.00% | (0.00) | |
| 6.3 | Mirror The Bare Glass Is As Long As The Counter. | ชุด | 2.00 | - | | | | | | | | | | | | | |
| 6.4 | Soap holder, paper | ชุด | 21.00 | 13,167.00 | 21.00 | 100.00% | 13,167.00 | - | 0.00% | - | - | 100.00% | 13,167.00 | - | 0.00% | (0.00) | |
| 6.5 | Clothes Rack | ชุด | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 6.6 | General Hand Shower | ชุด | - | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 6.7 | General Basin Faucet | ชุด | 14.00 | 35,000.00 | 14.00 | 100.00% | 35,000.00 | - | 0.00% | - | - | 100.00% | 35,000.00 | - | 0.00% | (0.00) | |
| 6.8 | Toilet Hose White | ชุด | 21.00 | 38,934.00 | 21.00 | 100.00% | 38,934.00 | - | 0.00% | - | - | 100.00% | 38,934.00 | - | 0.00% | (0.00) | |
| 6.9 | Low Toilet Faucet White | ชุด | 9.00 | 9,909.00 | 9.00 | 100.00% | 9,909.00 | - | 0.00% | - | - | 100.00% | 9,909.00 | - | 0.00% | (0.00) | |
| 6.1 | Floor Drain | ชุด | 21.00 | 14,196.00 | 21.00 | 100.00% | 14,196.00 | - | 0.00% | - | - | 100.00% | 14,196.00 | - | 0.00% | (0.00) | |
| 6.11 | Counter Domestic Granite Choose a color later (for sinks, toilets and men's toilets) | ม. | 14.25 | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | - | 0.00% | - | |
| 6.12 | Wall Hung Basin | ชุด | 2.00 | 8,700.00 | 2.00 | 100.00% | 8,700.00 | - | 0.00% | - | - | 100.00% | 8,700.00 | - | 0.00% | 0.00 | |
| 6.13 | General Basin Faucet | ชุด | 2.00 | 5,000.00 | 2.00 | 100.00% | 5,000.00 | - | 0.00% | - | - | 100.00% | 5,000.00 | - | 0.00% | 0.00 | |
| 6.14 | Mirror The Bare Glass Is As Long As The Counter. | ชุด | 3.00 | 39,000.00 | 3.00 | 100.00% | 39,000.00 | - | 0.00% | - | - | 100.00% | 39,000.00 | - | 0.00% | 0.00 | |
| 6.15 | Male Urinal | ชุด | 12.00 | 82,200.00 | 12.00 | 100.00% | 82,200.00 | - | 0.00% | - | - | 100.00% | 82,200.00 | - | 0.00% | (0.00) | |
| 6.16 | Urinal Flush Valve | ชุด | 12.00 | 72,000.00 | 12.00 | 100.00% | 72,000.00 | - | 0.00% | - | - | 100.00% | 72,000.00 | - | 0.00% | 0.00 | |
| Add.10 | Stop Valve | ชุด | 57.00 | 31,350.00 | 57.00 | 100.00% | 31,350.00 | - | 0.00% | - | - | 100.00% | 31,350.00 | - | 0.00% | (0.00) | |
| Add.11 | Bile Line | ชุด | 36.00 | 19,800.00 | 36.00 | 100.00% | 19,800.00 | - | 0.00% | - | - | 100.00% | 19,800.00 | - | 0.00% | 0.00 | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 6 : Sanitary Fixtures** | | | **507,821.00** | | **100.00%** | **507,821.00** | | **0.00%** | **-** | | **100.00%** | **507,821.00** | | **0.00%** | **0.00** | |
| **7** | **Door & Window** | | | | | | | | | | | | | | | | |
| | **Door** | | | | | | | | | | | | | | | | |
| 7.1 | D1- Double door size 11.90 x 4.20 m. | set | 1.00 | 363,643.00 | - | 90.00% | 327,278.70 | - | 10.00% | 36,364.30 | - | 100.00% | 363,643.00 | - | 0.00% | - | |
| 7.2 | D8 - Fire Rated Steel door size 1.50 x 2.05 m.(Double) | set | 3.00 | 91,608.00 | - | 90.00% | 82,447.20 | - | 10.00% | 9,160.80 | - | 100.00% | 91,608.00 | - | 0.00% | - | |
| 7.3 | D9 - Single Steel door size 1.00 x 2.05 m. (Single) | set | 3.00 | 40,839.00 | - | 90.00% | 36,755.10 | - | 10.00% | 4,083.90 | - | 100.00% | 40,839.00 | - | 0.00% | - | |
| 7.4 | D13 - Fire Rated Steel door size 1.00 x 2.05 m.(Single) | set | 5.00 | 91,310.00 | - | 90.00% | 82,179.00 | - | 10.00% | 9,131.00 | - | 100.00% | 91,310.00 | - | 0.00% | - | |
| 7.5 | D14 - Hatch Steel door size 1.00 x 1.00 m. | set | 1.00 | 12,000.00 | - | 90.00% | 10,800.00 | - | 10.00% | 1,200.00 | - | 100.00% | 12,000.00 | - | 0.00% | - | |
| 7.6 | D15 - Double steel door size 1.50 x 2.05 m.(Double) | set | 2.00 | 48,246.00 | - | 90.00% | 43,421.40 | - | 10.00% | 4,824.60 | - | 100.00% | 48,246.00 | - | 0.00% | - | |

**Bill Of Quantities**

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB RATCHADA.**
**ARCHITECTURAL WORKS**

| Item | Description | Unit | Qty. | Total Amount | Previous Accumlate | | | Work in This Period | | | Accumulate This Period | | | Remaining Work | | | Remark |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | Q'ty | % | Amount (Baht) | |
| | | | | | | | | | | | | | | | | | |
| 7.7 | SD1 - Shutter door size 1.00 x 1.4 m. | set | 1.00 | 43,000.00 | - | 90.00% | 38,700.00 | - | 10.00% | 4,300.00 | - | 100.00% | 43,000.00 | - | 0.00% | - | |
| 7.8 | HW_D8 Fire Rated Steel door size 1.50 x 2.05 m.(Double) | set | 3.00 | 23,673.00 | - | 90.00% | 21,305.70 | - | 10.00% | 2,367.30 | - | 100.00% | 23,673.00 | - | 0.00% | - | |
| 7.9 | HW_D9 Singl Steel door size 1.00 x 2.05 m. | set | 3.00 | 18,597.00 | - | 90.00% | 16,737.30 | - | 10.00% | 1,859.70 | - | 100.00% | 18,597.00 | - | 0.00% | - | |
| 7.1 | HW_D13 Fire Rated Steel door size 1.00 x 2.05 m.(Single) | set | 5.00 | 57,280.00 | - | 90.00% | 51,552.00 | - | 10.00% | 5,728.00 | - | 100.00% | 57,280.00 | - | 0.00% | - | |
| 7.11 | HW_D15 Double steel door size 1.50 x 2.05 m.(Double) | set | 2.00 | 22,352.00 | - | 90.00% | 20,116.80 | - | 10.00% | 2,235.20 | - | 100.00% | 22,352.00 | - | 0.00% | - | |
| | **WINDOW** | | | | | | | | | | | | | | | | |
| 7.12 | W1 - Window Size 10.10 x 3.00 m. | set | 1.00 | 112,594.73 | - | 90.00% | 101,335.26 | - | 10.00% | 11,259.47 | - | 100.00% | 112,594.73 | - | 0.00% | - | |
| 7.13 | W2 - Window Size 4.6 x 3.00 m. | set | 1.00 | 53,124.00 | - | 90.00% | 47,811.60 | - | 10.00% | 5,312.40 | - | 100.00% | 53,124.00 | - | 0.00% | - | |
| 7.14 | W3 - Window Size 4.4 x 3.00 m. | set | 1.00 | 51,355.00 | - | 90.00% | 46,219.50 | - | 10.00% | 5,135.50 | - | 100.00% | 51,355.00 | - | 0.00% | - | |
| 7.15 | W4 - Window Size 2.6 x 0.75 m. | set | 3.00 | 14,592.00 | - | 90.00% | 13,132.80 | - | 10.00% | 1,459.20 | - | 100.00% | 14,592.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 7 : Door & Window** | | | **1,044,213.73** | | **90.00%** | **939,792.36** | | **10.00%** | **104,421.37** | | **100.00%** | **1,044,213.73** | | **0.00%** | **-** | |
| **8** | **Stairs** | | | | | | | | | | | | | | | | |
| 8.1 | ST-01 GL1-2 (1st Floor-Deck) | | | | | | | | | | | | | | | | |
| 8.2 | - Thread width 0.27 x length 1.25 m (polished) | m. | 94.00 | 23,500.00 | - | 100.00% | 23,500.00 | - | 0.00% | - | - | 100.00% | 23,500.00 | - | 0.00% | - | |
| 8.3 | - Riser Height 0.2 x Length 1.25 m (Polished) | m. | 92.00 | 9,200.00 | - | 100.00% | 9,200.00 | - | 0.00% | - | - | 100.00% | 9,200.00 | - | 0.00% | - | |
| 8.4 | - nosing | m. | 98.50 | 39,400.00 | - | 100.00% | 39,400.00 | - | 0.00% | - | - | 100.00% | 39,400.00 | - | 0.00% | - | |
| 8.5 | - Landing | sq.m | 23.40 | 7,347.60 | - | 100.00% | 7,347.60 | - | 0.00% | - | - | 100.00% | 7,347.60 | - | 0.00% | - | |
| 8.6 | - Plaster side | sq.m | 57.00 | 13,680.00 | - | 100.00% | 13,680.00 | - | 0.00% | - | - | 100.00% | 13,680.00 | - | 0.00% | - | |
| 8.7 | - Panting | sq.m | 57.00 | 8,550.00 | - | 100.00% | 8,550.00 | - | 0.00% | - | - | 100.00% | 8,550.00 | - | 0.00% | - | |
| 8.8 | - railing | m. | 74.00 | 148,000.00 | - | 100.00% | 148,000.00 | - | 0.00% | - | - | 100.00% | 148,000.00 | - | 0.00% | - | |
| | Granite entrance stairs with a material price not exceeding 2,000 baht per square meter | | | | | | | | | | | | | | | | |
| 8.9 | - Thread กว้าง 0.30 เมตร | m. | 30.40 | 30,400.00 | - | 100.00% | 30,400.00 | - | 0.00% | - | - | 100.00% | 30,400.00 | - | 0.00% | - | |
| 8.1 | - Riser สูง 0.15 เมตร | m. | 38.00 | 38,000.00 | - | 100.00% | 38,000.00 | - | 0.00% | - | - | 100.00% | 38,000.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 8 : Stair work** | | | **318,077.60** | | **100.00%** | **318,077.60** | | **0.00%** | **-** | | **100.00%** | **318,077.60** | | **0.00%** | **-** | |
| **9** | **Additional Work** | | | | | | | | | | | | | | | | |
| 9.1 | termites pest control | sq.m | 1,310.00 | 288,200.00 | - | 100.00% | 288,200.00 | - | 0.00% | - | - | 100.00% | 288,200.00 | - | 0.00% | - | |
| 9.2 | Curb Toilet Room | m | 148.00 | 30,932.00 | - | 100.00% | 30,932.00 | - | 0.00% | - | - | 100.00% | 30,932.00 | - | 0.00% | - | |
| 9.3 | Water Proof Toilet | sq.m | 161.00 | 46,046.00 | - | 100.00% | 46,046.00 | - | 0.00% | - | - | 100.00% | 46,046.00 | - | 0.00% | - | |
| | | | | | | | | | | | | | | | | | |
| | **Sum Item 9 : Additional Work** | | | **365,178.00** | | **100.00%** | **365,178.00** | | **0.00%** | **-** | | **100.00%** | **365,178.00** | | **0.00%** | **-** | |

**Project  Atlas Superclub Ratchada.**

**Structure work and Architecture work**

**Owner: HW Group / Ratchada Entertainment**

**Monthly Report**
**Period 1 December 2025 - 31 Dceember 2025**

**BY**

**Italain-Thai Development Public Limited**
**2034/132-161ITALTAHITOWER,**
**NEWPETCHBURIROAD,BANGKAPI, HUAYKWANG,BANGKOK10310, THAILAND**

# SECTION

1. Executive Summary
    1.1 Project Information
    1.2 Excutive  Summarise of work progress
    1.3 Organization Chart

| | | |
|---|---|---|
| **Project** | **:** | **ATLAS SUPERCLUB** |
| **Owner** | **:** | **HW Group / Ratchada Entertainment** |
| **Consultant** | **:** | **CMP Management Asia Co., Ltd** |
| **Contractor** | **:** | **Italian-Thai Development Pcl.** |

| | |
|---|---|
| Project Details | : Construction of a 2-story building |
| Project Location | : 58 Ratchadaphisek Road, Soi 4, Huai Khwang Subdistrict, Bangkok |
| Estimated construction area | : 1,810 Sq.m. |
| Type and number of buildings | : Reinforced concrete building, 2 stories high (excluding rooftop) and 1 basement floor, steel frame roof frame. |
| Scope of work | : Structural and architectural works |
| Project Value | : 56,000,000.00 Baht |
| Project Start Date | : 1 May 2024 |
| Project End Date | : 8 December 2025 |
| Total project implementation period | : 587 Day |
| Project owner company | : Ratchada Entertainment Group Co., Ltd. |
| Architectural Design Company | : D&A Design Co., Ltd. |
| Structural Engineering Design Company | : D&A Design Co., Ltd. |
| Building assembly system engineering design company | : Me-Decons Co., Ltd. |
| Project Principal Contractor Company | : Italian -Thai Development Public Company Limited |

## Excutive Summarise of work progress

**PROJECT : ATLAS DUPERCLUB**

**DATE UPDATE :** 29-01-26

| Overall Progress | Last Month | This Month | | Ahead(+)/Delay(-) |
|---|---|---|---|---|
| | | Plan | Actual | ( % ) |
| | 100.00% | 100.00% | 100.00% | 0.00% |

| | | |
|---|---|---|
| Project Start | 01 May 2024 | |
| Project Completion | 30 November 2025 | |
| Project Duration | 579 | Days |
| Elapsed Time | 638 | Days |
| Ahead (+)/Delay(-) | 0.00 | Day |

**Work Progress**

1 Aluminium Door
2 Insulation Ceiling
3 Casting concrete lean for slab

| Avg. Manpower per day | | |
|---|---|---|
| | : Last Month | 40 |
| | : This Month | 40 |
| | : Next Month | 10 |

## S-Curve

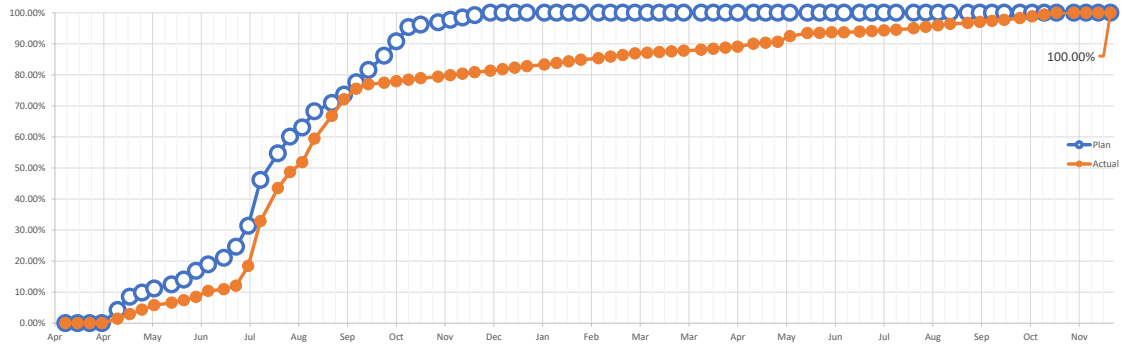


## Project cost Progress

| | Description | Contract Cost | Weight(%) | Progress(%) | Remark |
|---|---|---|---|---|---|
| 1 | **Preliminaries** | **4,755,448.70** | **8.49%** | **8.49%** | |
| | Site Mobilization and Preparation | 568,000.00 | 1.01% | 1.01% | |
| | Office&Store Construction | 102,600.00 | 0.18% | 0.18% | |
| | Work Shop Construction | 29,200.00 | 0.05% | 0.05% | |
| | Utilities & Facilities | 645,048.70 | 1.15% | 1.15% | |
| | Temporary Fence & Facilities | 757,300.00 | 1.35% | 1.35% | |
| | Non Productive Labour | 2,326,000.00 | 4.15% | 4.15% | |
| | Service and General Expense | 327,300.00 | 0.58% | 0.58% | |
| 2 | **Structural work** | **29,794,860.40** | **53.21%** | **53.21%** | |
| | Piling works | 3,364,600.00 | 6.01% | 6.01% | |
| | Foundation | 534,957.00 | 0.96% | 0.96% | |
| | Beam | 789,546.00 | 1.41% | 1.41% | |
| | Slab | 4,635,294.00 | 8.28% | 8.28% | |
| | Column | 829,243.00 | 1.48% | 1.48% | |
| | Steel Structure | 14,526,900.00 | 25.94% | 25.94% | |
| | Watertank / M&E Room | 1,813,564.00 | 3.24% | 3.24% | |
| | Stairs | 719,259.00 | 1.28% | 1.28% | |
| | Concrete Fin | 1,588,231.40 | 2.84% | 2.84% | |
| | Platform for MEP Works in Roof Void | 544,690.00 | 0.97% | 0.97% | |
| | Lift Core | 242,676.00 | 0.43% | 0.43% | |
| | Support Frame (Door & Window) | 205,900.00 | 0.37% | 0.37% | |
| 3 | **Architectural Works** | **16,791,095.33** | **29.98%** | **29.98%** | |
| | Roof Finishes | 1,901,158.00 | 3.39% | 3.39% | |
| | Floor Finishes | 1,854,970.00 | 3.31% | 3.31% | |
| | Wall & Wall Finishes | 8,263,927.00 | 14.76% | 14.76% | |
| | Ceiling | 1,805,400.00 | 3.22% | 3.22% | |
| | Painting Finishes | 730,350.00 | 1.30% | 1.30% | |
| | Sanitary Fixtures | 507,821.00 | 0.91% | 0.91% | |
| | Door | 1,044,213.73 | 1.86% | 1.86% | |
| | Stair | 318,077.60 | 0.57% | 0.57% | |
| | Additional Work | 365,178.00 | 0.65% | 0.65% | |
| 4 | **Overhead and Profit** | **4,658,595.57** | **8.32%** | **8.32%** | |
| | | | | | |
| **Accumulate Progress** | | **56,000,000.00** | **100.00%** | **100.00%** | |

| Document Status | Submit | | | Status | | | Status Outstanding | Remark |
|---|---|---|---|---|---|---|---|---|
| | Last Month | This Month | Total | Approve | Disapprove | Seen | | |
| | | | | | | | | |
| RFI | 2 | 0 | 2 | 0 | 0 | 2 | 0 | |
| RFA | 92 | 0 | 92 | 61 | 31 | 92 | 0 | All approve as note |
| | | | | | | | | |

**Problem & Obstruction**

# ORGANIZATION CHART

J2596 ATLAS SUPERCLUB RATCHADA

**PROJECT ENGINEER**

MR.DANAI SUWANMANEE
Tel. 087-110-4750

**SAEETY OFFICER**

MS.Jarinthon L.
Tel. 062-025-5440

**SECRETARY**

MRS.NATCHA R.
Tel. 089-802-4268

**ST ENGINEER**

MR.SOMBOON S.
Tel. 098-452-6283

**M&E ENGINEER**

MR.NUPONG T.
Tel. 064-231-6384

**ARCHITECTUR**

MS.KESSIRIN M.
Tel. 090-969-6396

**COST ENGINEER**

MR.PANUPAS S.
Tel. 087-165-7318

**QS ENGINEER**

MS.PEERAYA P.
Tel. 094-495-5483

**Accountant / Admin**

MRS.CHOTIKA B.
Tel. 085-259-3737

**STORE**

MR.KITIPONG C.
Tel. 092-975-1810

**Personnel**

MR.WUTTICHAI K.
Tel. 084-376-7642

**Purchaser**

MRS.KANITA S.
Tel. 081-454-2886

# SECTION

**2. Work performed and completed in the reporting month**

- **2.1 Progress of work**
- **2.2 Man power schedules**
- **2.3 Equipment schedules**
- **2.4 Weather**

| | | |
|---|---|---|
| **Project** | **:** | **ATLAS SUPERCLUB** |
| **Owner** | **:** | **HW Group / Ratchada Entertainment** |
| **Consultant** | **:** | **CMP Management Asia Co., Ltd** |
| **Contractor** | **:** | **Italian-Thai Development Pcl.** |

**TALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB**
**BUILDING 5**

# Manpower Report

| Manpower | Dec 25 | | | | Dec 25 | | | | | | | Dec 25 | | | | | | | Dec 25 | | | | | | | Dec 25 | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed |
| | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 | 20 | 21 | 22 | 23 | 24 | 25 | 26 | 27 | 28 | 29 | 30 | 31 |
| **ITD** | **10** | **8** | **8** | **6** | **8** | **8** | **10** | **10** | **8** | **8** | **6** | **8** | **8** | **10** | **10** | **8** | **8** | **6** | **8** | **8** | **10** | **10** | **8** | **8** | **6** | **8** | **8** | **3** | **2** | **2** | **2** |
| General Labor | 7 | 5 | 5 | 3 | 5 | 5 | 7 | 7 | 5 | 5 | 3 | 5 | 5 | 7 | 7 | 5 | 5 | 3 | 5 | 5 | 7 | 7 | 5 | 5 | 3 | 5 | 5 | - | - | - | - |
| Security Guard | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 |
| Driver | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Subcontractor** | **15** | **15** | **15** | **15** | **20** | **15** | **7** | **15** | **15** | **15** | **15** | **15** | **15** | **-** | **15** | **15** | **15** | **15** | **15** | **15** | **-** | **15** | **15** | **15** | **15** | **15** | **15** | **8** | **-** | **-** | **-** |
| **AR** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **-** | **4** | **4** | **4** | **4** | **4** | **4** | **-** | **4** | **4** | **4** | **4** | **4** | **4** | **-** | **-** | **-** | **-** |
| **CNE** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** |
| Site Engineer | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Worker | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **KPSK** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **4** | **-** | **4** | **4** | **4** | **4** | **4** | **4** | **-** | **4** | **4** | **4** | **4** | **4** | **4** | **-** | **-** | **-** | **-** |
| Foreman | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Worker | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | - | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Wall** | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Floor** | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Sanitary** | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **ST** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **-** | **3** | **3** | **3** | **3** | **3** | **3** | **-** | **3** | **3** | **3** | **3** | **3** | **3** | **-** | **-** | **-** | **-** |
| **SRN** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** |
| Foreman | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Worker | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **PR** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **-** | **3** | **3** | **3** | **3** | **3** | **3** | **-** | **3** | **3** | **3** | **3** | **3** | **3** | **-** | **-** | **-** | **-** |
| Site Engineer | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Worker | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | - | 3 | 3 | 3 | 3 | 3 | 3 | - | 3 | 3 | 3 | 3 | 3 | 3 | - | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Scaffloding** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** |
| **Anesco** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** | **-** |
| Site Engineer | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Worker | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Façade** | **8** | **8** | **8** | **8** | **13** | **8** | **-** | **8** | **8** | **8** | **8** | **8** | **8** | **-** | **8** | **8** | **8** | **8** | **8** | **8** | **-** | **8** | **8** | **8** | **8** | **8** | **8** | **8** | **-** | **-** | **-** |
| Worker Install Steel Structure | - | - | - | - | 5 | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Worker Install GRC | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | 4 | - | - | - |
| Worker Painting | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | - | 4 | 4 | 4 | 4 | 4 | 4 | 4 | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Sum ITD** | **25** | **23** | **23** | **21** | **28** | **23** | **17** | **25** | **23** | **23** | **21** | **23** | **23** | **10** | **25** | **23** | **23** | **21** | **23** | **23** | **10** | **25** | **23** | **23** | **21** | **23** | **23** | **11** | **2** | **2** | **2** |

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB**
**BUILDING 5**

# Equipment Report

| Machine | Dec 25 | | | | Dec 25 | | | | | | | Dec 25 | | | | | | | Dec 25 | | | | | | | Dec 25 | | | | | | Jan 26 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed | Thu | Fri | Sat | Sun | Mon | Tue | Wed | Thu |
| | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 | 20 | 21 | 22 | 23 | 24 | 25 | 26 | 27 | 28 | 29 | 30 | 31 | 1 |
| **SITE** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** |
| Total station | 1 | 1 | 1 | 1 | 1 | 1 | 1 | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Auto level | 1 | 1 | 1 | 1 | 1 | 1 | 1 | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| fiber cutting machine | 1 | 1 | 1 | 1 | 1 | 1 | 1 | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Welding cabinet | 2 | 2 | 2 | 2 | 2 | 2 | 2 | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| gas cutting set | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 |
| 6 wheel vehicle | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 |
| backhoe | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Electrical 6 wheel vehicl | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Subcontractor** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** | **3** |
| Backhoe | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Mobile Crane | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Boom Lift | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 |
| X lift | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Spider Crane | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Office** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** | **2** |
| Pickup Survice | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 |
| Pickup PM | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| **Machine TOTAL** | **12** | **12** | **12** | **12** | **12** | **12** | **12** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** | **7** |

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB**
**BUILDING 5**

# Weather Report

**2025**

| Sun | Mon | Tue | | | | |
|---|---|---|---|---|---|---|
| | 1 Dec | 2 Dec | 3 Dec | 4 Dec | 5 Dec | 6 Dec |
| 7 Dec | 8 Dec | 9 Dec | 10 Dec | 11 Dec | 12 Dec | 13 Dec |
| 14 Dec | 15 Dec | 16 Dec | 17 Dec | 18 Dec | 19 Dec | 20 Dec |
| 21 Dec | 22 Dec | 23 Dec | 24 Dec | 25 Dec | 26 Dec | 27 Dec |
| 28 Dec | 29 Dec | 30 Dec | 31 Dec | | | |

# SECTION

## 3. Status of construction work

| | | |
|---|---|---|
| **Project** | **:** | **ATLAS SUPERCLUB** |
| **Owner** | **:** | **HW Group / Ratchada Entertainment** |
| **Consultant** | **:** | **CMP Management Asia Co., Ltd** |
| **Contractor** | **:** | **Italian-Thai Development Pcl.** |

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB**
**BUILDING 5**

## Status of work progress

Date Update : 29-01-26

| | | |
|---|---|---|
| Project Start : | 01 May 2024 | |
| Project Completion : | 30 September 2025 | |
| Project Duration : | 518 | Days |
| Elapsed Time : | 632 | Days |
| Ahead (+)/Delay(-) : | 0.00 | Days |

| Description | This Month | | | Ahead(+)/Delay(-) |
|---|---|---|---|---|
| | Last Month | Plan | Actual | % |
| | | | | |
| All Progress | 100.00% | 100.00% | 100.00% | 0.00% |
| | | | | |

Remark :

# SECTION

## 4. Monthly Progress Plan: S-Curve

| | | |
|---|---|---|
| **Project** | **:** | **ATLAS SUPERCLUB** |
| **Owner** | **:** | **HW Group / Ratchada Entertainment** |
| **Consultant** | **:** | **CMP Management Asia Co., Ltd** |
| **Contractor** | **:** | **Italian-Thai Development Pcl.** |

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**

**PROJECT : ATLAS SUPERCLUB**

**BUILDING 5**

| Item | Description | Amount Plan | Amount Actual | Duration | As of Jun 24 % | | May W1 | May W2 | May W3 | May W4 | June W1 | June W2 | June W3 | June W4 | July W1 | July W2 | July W3 | July W4 | August W1 | August W2 | August W3 | August W4 | September W1 | September W2 | September W3 | September W4 | October W1 | October W2 | October W3 | October W4 | November W1 | November W2 | November W3 | November W4 | December W1 | December W2 | December W3 | December W4 | January W1 | January W2 | January W3 | January W4 | February W1 | February W2 | February W3 | February W4 | March W1 | March W2 | March W3 | March W4 | April W1 | April W2 | April W3 | April W4 | May W1 | May W2 | May W3 | May W4 | June W1 | June W2 | June W3 | June W4 | July W1 | July W2 | July W3 | July W4 | August W1 | August W2 | August W3 | August W4 | September W1 | September W2 | September W3 | September W4 | October W1 | October W2 | October W3 | October W4 | November W1 | November W2 | November W3 | November W4 | December W1 | December W2 | December W3 | December W4 | Sum | Ramark |
|---|---|---

# SECTION

**5. Summary of matters related to the contract**

**5.1 Claims**

**5.2 Disbursement of annuity**

**5.3 Status of the task Increase - Decrease**

| | | |
|---|---|---|
| **Project** | **:** | **ATLAS SUPERCLUB** |
| **Owner** | **:** | **HW Group / Ratchada Entertainment** |
| **Consultant** | **:** | **CMP Management Asia Co., Ltd** |
| **Contractor** | **:** | **Italian-Thai Development Pcl.** |

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB**
**BUILDING 5**

**Summarize various issues related to the contract**

| Items | Description | Stetus | Remarks |
|---|---|---|---|
| | | | |
| **5.1** | **Claim Status** | | |
| 1 | 1.0/ITD/ASC/Payment/018 Date 29 Jan 26 | | |
| | Request for approval payment Claim No. 18 | | |
| | | | |
| **5.2** | **Annuity disbursement status** | | |
| 1 | 1.0/ITD/ASC/Payment/001 Date 7 Jun 24 | Approve | |
| | Request for approval payment Claim No. 1 | | |
| 2 | 1.0/ITD/ASC/Payment/002 Date 8 Jul 24 | Approve | |
| | Request for approval payment Claim No. 2 | | |
| 3 | 1.0/ITD/ASC/Payment/003 Date 7 Aug 24 | Approve | |
| | Request for approval payment Claim No. 3 | | |
| 4 | 1.0/ITD/ASC/Payment/004 Date 5 Sep 24 | Approve | |
| | Request for approval payment Claim No. 4 | | |
| 5 | 1.0/ITD/ASC/Payment/005 Date 10 Oct 24 | Approve | |
| | Request for approval payment Claim No. 5 | | |
| 6 | 1.0/ITD/ASC/Payment/006 Date 9 Nov 24 | Approve | |
| | Request for approval payment Claim No. 6 | | |
| 7 | 1.0/ITD/ASC/Payment/007 Rev.1 Date 23 Dec 24 | Approve | |
| | Request for approval payment Claim No. 7 | | |
| 8 | 1.0/ITD/ASC/Payment/008 Date 16 Jan 25 | Approve | |
| | Request for approval payment Claim No. 8 | | |
| 9 | 1.0/ITD/ASC/Payment/009 Date 20 Feb 25 | Approve | |
| | Request for approval payment Claim No. 9 | | |
| 10 | 1.0/ITD/ASC/Payment/010 Date 20 Mar 25 | Approve | |
| | Request for approval payment Claim No. 10 | | |
| 11 | 1.0/ITD/ASC/Payment/010 Date 21 Apr 25 | Approve | |
| | Request for approval payment Claim No. 11 | | |
| 12 | 1.0/ITD/ASC/Payment/012 Date 20 May 25 | Approve | |
| | Request for approval payment Claim No. 12 | | |
| 13 | 1.0/ITD/ASC/Payment/013 Date 20 Jun 25 | Approve | |
| | Request for approval payment Claim No. 13 | | |
| 14 | 1.0/ITD/ASC/Payment/014 Date 21 Aug 25 | Approve | |
| | Request for approval payment Claim No. 14 | | |
| 15 | 1.0/ITD/ASC/Payment/015 Date 25 Sep 25 | Approve | |
| | Request for approval payment Claim No. 15 | | |
| 16 | 1.0/ITD/ASC/Payment/016 Date 25 Oct 25 | Approve | |
| | Request for approval payment Claim No. 16 | | |
| 17 | 1.0/ITD/ASC/Payment/017 Date 25 Nov 25 | Approve | |
| | Request for approval payment Claim No. 17 | | |
| | | | |
| | | | |
| | | | |
| | | | |

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB**
**BUILDING 5**

**Summarize various issues related to the contract**

| Items | Description | Stetus | Remarks |
|---|---|---|---|
| | | | |
| **5.3** | **Summary of the status of Variation Order** | | |
| 1 | 1.0/ITD/ASC/Payment (VO)/001 Rev.1 Date 11 Dec 24 | Approve | |
| | Request for approval payment Claim No. 1 | | |
| 2 | 1.0/ITD/ASC/Payment (VO)/002 Date 24 Jun 25 | Canceled | |
| | Request for approval payment Claim No. 2 | | |
| 3 | 1.0/ITD/ASC/Payment (VO)/003 Date 20 Feb 25 | Approve | |
| | Request for approval payment Claim No. 3 | | |
| 4 | 1.0/ITD/ASC/Payment (VO)/004 Date 25 Feb 25 | Approve | |
| | Request for approval payment Claim No. 4 | | |
| 5 | 1.0/ITD/ASC/Payment (VO)/005 Date 20 Mar 25 | Approve | |
| | Request for approval payment Claim No. 5 | | |
| 6 | 1.0/ITD/ASC/Payment (VO)/006 Date 20 May 25 | Approve | |
| | Request for approval payment Claim No. 6 | | |
| 7 | 1.0/ITD/ASC/Payment (VO)/007 Date 20 Jun 25 | Approve | |
| | Request for approval payment Claim No. 7 | | |
| 8 | 1.0/ITD/ASC/Payment (VO)/008 Date 20 Jun 25 | Approve | |
| | Request for approval payment Claim No. 8 | | |
| 9 | 1.0/ITD/ASC/Payment (VO)/009 Date 20 Jul 25 | Approve | |
| | Request for approval payment Claim No. 9 | | |
| 10 | 1.0/ITD/ASC/Payment (VO)/010 Date 21 Aug 25 | Approve | |
| | Request for approval payment Claim No. 10 | | |
| 11 | 1.0/ITD/ASC/Payment (VO)/011 Date 25 Sep 25 | Approve | |
| | Request for approval payment Claim No. 11 | | |
| 12 | 1.0/ITD/ASC/Payment (VO)/012 Date 25 Oct 25 | Approve | |
| | Request for approval payment Claim No. 12 | | |
| 13 | 1.0/ITD/ASC/Payment (VO)/013 Date 25 Nov 25 | Approve | |
| | Request for approval payment Claim No. 13 | | |
| 14 | 1.0/ITD/ASC/Payment (VO)/013 Date 29 Jan 26 | | |
| | Request for approval payment Claim No. 14 | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |

# SECTION

## 6. Problems encountered and solutions

| | | |
|---|---|---|
| **Project** | **:** | **ATLAS SUPERCLUB** |
| **Owner** | **:** | **HW Group / Ratchada Entertainment** |
| **Consultant** | **:** | **CMP Management Asia Co., Ltd** |
| **Contractor** | **:** | **Italian-Thai Development Pcl.** |

**ITALIAN-THAI DEVELOPMENT PUBLIC COMPANY LIMITED**
**PROJECT : ATLAS SUPERCLUB**
**BUILDING 5**

## Problems and obstacles encountered and solutions

| Items | Description | Problem solving solution | Remarks |
|---|---|---|---|
| | | | |
