Bangkok Dec-Con Public Company Limited

52/3 Moo 8, Bangbuatong-Supanburi Road La Han Sub-District

Bang Bua Thong District Nonthaburi, 11110. Thailand

TAX.ID 0107554000178

Project : ATLAS SUPERCLUB @ Ratchada Soi 4

No 09 12 February 2026

INVOICE

Customer Ratchada Entertainment Group Co., Ltd. TAX ID. 0105566107710

Address 58 Ratchadaphisek Road, Soi 4, Huaykhwang Subdistrict,

Huaykhwang District, Bangkok, Thailand 10310

No.	Description	Amount
A	Interim Payment No.9	8,100,795.09
B	Less Advance Payment 40%	3,240,318.04
C	Total Payment	4,860,477.05
D	Less Retention 5%	405,039.75
E	Total	4,455,437.30
F	VAT 7%	340,233.40
G	Total Payment (Include VAT)	4,795,670.70
H	Less Withholding Tax 3%	145,814.31
I	Net Payment	**4,649,856.39**

(Four million six hundred forty-nine thousand eight hundred fifty-six baht and thirty-nine satang).

Authorized Signature .....

(Mr. Thanapon Wittayaphon)

Project Manager

Company : Bangkok Dec-Con Public Company Limited

PROJECT : ATLAS SUPERCLUB RATCHADA.

SUMMARY OF PAYMENT CLAIM

Payment Claim No 9

February 12, 2026

Item	Description	Unit	Contract			Previous Period Claim		This month Claim		Cumulative to date		Remaining Balances	
			QTY.	BKD	%	Total	%	Total	%	Total	%	Total	%
	Summary of construction costs of the project.												
A	ID Works	LS	1	69,967,924.00	100.00%	62,735,071.25	89.66%	7,232,852.75	10.34%	69,967,924.00	100.00%	-	0.00%
C	Preliminary Cost	LS	1	3,512,100.00	100.00%	3,512,100.00	100.00%	-	0.00%	3,512,100.00	100.00%	-	0.00%
D	Overhead and Profit	LS	1	8,396,150.88	100.00%	7,528,208.54	89.66%	867,942.34	10.34%	8,396,150.88	100.00%	(0.00)	0.00%
E	**Summary (A+B+C+D)**			**81,876,174.88**	**100.00%**	**73,775,379.79**	**90.11%**	**8,100,795.09**	**9.89%**	**81,876,174.88**	**100.00%**	**(0.00)**	**0.00%**
G	Less Advance Payment 40.00 %			32,750,469.95	100.00%	29,510,151.92	90.11%	3,240,318.03	9.89%	32,750,469.95	100.00%	(0.00)	0.00%
H	**Total (E+F-G)**			**49,125,704.93**	**100.00%**	**44,265,227.87**	**90.11%**	**4,860,477.06**	9.89%	**49,125,704.93**	**100.00%**	**0.00**	**0.00%**
I	Vat 7%			3,438,799.35	100.00%	3,098,565.95	90.11%	340,233.40	9.89%	3,438,799.35	100.00%	(0.00)	0.00%
J	**Include Vat (H+I)**			**52,564,504.28**	**100.00%**	**47,363,793.83**	**90.11%**	**5,200,710.45**	**9.89%**	**52,564,504.28**	**100.00%**	**(0.00)**	**0.00%**
K	Retention 5% Of (E)			4,093,808.74	100.00%	3,688,768.99	90.11%	405,039.75	9.89%	4,093,808.74	100.00%	0.00	0.00%
L	**Total Less Retention (J-K)**			**48,470,695.54**	**100.00%**	**43,675,024.83**	**90.11%**	**4,795,670.71**	**9.89%**	**48,470,695.54**	**100.00%**	**0.00**	**0.00%**
M	Withholding Tax 3% Of (H)			1,473,771.15	100.00%	1,327,956.86	90.11%	145,814.29	9.89%	1,473,771.15	100.00%	(0.00)	0.00%
N	**Net Payment (L+M)**			**46,996,924.39**	**100.00%**	**42,347,067.98**	**90.11%**	**4,649,856.41**	**9.89%**	**46,996,924.39**	**100.00%**	**0.00**	**0.00%**

(Mr. Thanapon Wittayaphon)

Project Manager

BANGKOK DEC-CON PUBLIC COMPANY LIMITED

Date...../...../.....2026.....

(Mr. Clarence Sim)

Project Consultant

CMP Management ASIA CO., LTD.

Date...../...../.....

Progress Claim 09

PROJECT : ATLAS SUPER CLUB

SUBJECT : INTERIOR

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

No. **BKD/ASC/Payment/009**

DATE : 13/2/2569

ITEM	DESCRIPTION	QUANTITY	UNIT	AMOUNT (BAHT)	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARK
					%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
	INTERIOR WORK												
1	SEATING AREA	1	UNIT	19,575,757.00	89.64%	17,548,268.25	10.36%	2,027,488.75	100.00%	19,575,757.00	0.00%	-	
2	MAIN BAR AREA	1	UNIT	4,269,365.00	90.00%	3,842,428.50	10.00%	426,936.50	100.00%	4,269,365.00	0.00%	-	
3	LOBBY AREA + LOBBY W.C.	1	UNIT	3,757,224.00	87.30%	3,280,025.30	12.70%	477,198.70	100.00%	3,757,224.00	0.00%	-	
4	GREETER AREA	1	UNIT	1,355,787.00	89.69%	1,215,984.30	10.31%	139,802.70	100.00%	1,355,787.00	0.00%	-	
5	MAIN W.C. FOYER AREA	1	UNIT	701,492.00	89.35%	626,760.60	10.65%	74,731.40	100.00%	701,492.00	0.00%	-	
6	MAIN W.C. (PUBLIC AREA)	1	UNIT	5,214,311.00	87.43%	4,559,013.90	12.57%	655,297.10	100.00%	5,214,311.00	0.00%	-	
7	VIP 1	1	UNIT	5,843,263.00	90.53%	5,289,639.30	9.47%	553,623.70	100.00%	5,843,263.00	0.00%	-	
8	VIP 2	1	UNIT	10,722,856.00	90.31%	9,683,762.40	9.69%	1,039,093.60	100.00%	10,722,856.00	0.00%	-	
9	VIP 3	1	UNIT	7,914,741.00	90.18%	7,137,373.50	9.82%	777,367.50	100.00%	7,914,741.00	0.00%	-	
10	3 VIP W.C.s	1	UNIT	986,858.00	90.00%	888,172.20	10.00%	98,685.80	100.00%	986,858.00	0.00%	-	
11	VIP CORRIDOR AREA	1	UNIT	1,805,572.00	90.00%	1,625,014.80	10.00%	180,557.20	100.00%	1,805,572.00	0.00%	-	
	PROVISIONAL SUM												
12	PRO-SUM TILE	1	UNIT	807,180.00	90.00%	726,462.00	10.00%	80,718.00	100.00%	807,180.00	0.00%	-	
13	PRO-SUM DECORATIVE COLUMN	1	UNIT	5,909,647.00	90.00%	5,318,682.30	10.00%	590,964.70	100.00%	5,909,647.00	0.00%	-	
14	PRO-SUM RAILING/BALUSTRADE	1	UNIT	1,103,871.00	90.00%	993,483.90	10.00%	110,387.10	100.00%	1,103,871.00	0.00%	-	
	TOTAL COST			69,967,924.00	89.66%	62,735,071.25	10%	7,232,852.75	100.00%	69,967,924.00	0.00%	-	
	PRELIM	0%		3,512,100.00		3,512,100.00				3,512,100.00		- 0.00	
	OVERHEAD	12%		8,396,150.88		7,528,208.54		867,942.34		8,396,150.88		-	
	TOTAL			**81,876,174.88**	**90%**	**73,775,379.79**	10%	8,100,795.09	**100%**	**81,876,174.88**	**0%**	**- 0.00**	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB

SUBJECT : INTERIOR

DATE : 12/2/2026

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	DESCRIPTION	QUANTITY	UNIT	TOTAL	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARK
					%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
	PRELIMINARIES AND SPECIFIC CONDITIONS												
1.0	TEMPORARY PROTECTION FOR WORK AND HANDOVER	1	UNIT	70,200.00	100.00%	70,200.00		-	100.00%	70,200.00	0.00%	0.00	
2.0	WORKING HOURS (OVER TIME)	1	UNIT	175,600.00	100.00%	175,600.00		-	100.00%	175,600.00	0.00%	0.00	
3.0	DOCUMENT (IE. WORKING PROGRAMME, PICTURE, REPORT AND ETC.)	1	UNIT	35,100.00	100.00%	35,100.00		-	100.00%	35,100.00	0.00%	0.00	
4.0	SITE PROTECTION OF PUBLIC AND PRIVATE SERVICE	1	UNIT	87,800.00	100.00%	87,800.00		-	100.00%	87,800.00	0.00%	0.00	
5.0	WATER SUPPLY	1	UNIT	52,700.00	100.00%	52,700.00		-	100.00%	52,700.00	0.00%	0.00	
6.0	ELECTRICITY SUPPLY	1	UNIT	175,600.00	100.00%	175,600.00		-	100.00%	175,600.00	0.00%	0.00	
7.0	TRANSPORTATION AND MOVING MATERIAL	1	UNIT	140,500.00	100.00%	140,500.00		-	100.00%	140,500.00	0.00%	0.00	
8.0	TEMPORARY LIGHTING FOR OWN USE AND PUBLIC AREA	1	UNIT	105,400.00	100.00%	105,400.00		-	100.00%	105,400.00	0.00%	0.00	
9.0	CONTRACTOR ALL RISK	1	UNIT	158,100.00	100.00%	158,100.00		-	100.00%	158,100.00	0.00%	0.00	
10.0	FIRST DEDUCT	1	UNIT	35,100.00	100.00%	35,100.00		-	100.00%	35,100.00	0.00%	0.00	
11.0	COORDINATE WITH OTHER CONTRACTOR AND SUPPLIER	1	UNIT	35,100.00	100.00%	35,100.00		-	100.00%	35,100.00	0.00%	0.00	
12.0	FIRE PREVENTION AND TEMPORARY FIRE PROTECTION	1	UNIT	35,100.00	100.00%	35,100.00		-	100.00%	35,100.00	0.00%	0.00	
13.0	CLEANING EXPENSES	1	UNIT	158,100.00	100.00%	158,100.00		-	100.00%	158,100.00	0.00%	0.00	
14.0	DEBRIS REMOVING TO OUTSIDE	1	UNIT	87,800.00	100.00%	87,800.00		-	100.00%	87,800.00	0.00%	0.00	
15.0	BOND	1	UNIT	70,200.00	100.00%	70,200.00		-	100.00%	70,200.00	0.00%	0.00	
16.0	TAXATION	1	UNIT	70,200.00	100.00%	70,200.00		-	100.00%	70,200.00	0.00%	0.00	
17.0	SURVEY AND LAYOUT COSTS	1	UNIT	70,200.00	100.00%	70,200.00		-	100.00%	70,200.00	0.00%	0.00	
18.0	TEMPORARY STORAGE COSTS	1	UNIT	52,700.00	100.00%	52,700.00		-	100.00%	52,700.00	0.00%	0.00	
19.0	TRANSPORTATION COSTS FOR WORKERS	1	UNIT	140,500.00	100.00%	140,500.00		-	100.00%	140,500.00	0.00%	0.00	
20.0	SHOP DRAWING AND AS-BUILT DRAWINGS	1	UNIT	316,100.00	100.00%	316,100.00		-	100.00%	316,100.00	0.00%	0.00	
21.0	FIELD STAFF EXPENSES	1	UNIT	825,400.00	100.00%	825,400.00			100.00%	825,400.00	0.00%	0.00	
22.0	EXPENSES FOR SITE OFFICE EQUIPMENT	1	UNIT	70,200.00	100.00%	70,200.00		-	100.00%	70,200.00	0.00%	0.00	
23.0	EXPENSES FOR COLLECTING WORK	1	UNIT	175,600.00	100.00%	175,600.00		-	100.00%	175,600.00	0.00%	0.00	
24.0	EXPENSES FOR WORKERS AT THE WORK SITE	1	UNIT	105,400.00	100.00%	105,400.00		-	100.00%	105,400.00	0.00%	0.00	
25.0	INTERNET SYSTEM RENTAL FEE	1	UNIT	52,700.00	100.00%	52,700.00		-	100.00%	52,700.00	0.00%	0.00	
26.0	EXPENSES FOR SCAFFOLDING	1	UNIT	210,700.00	100.00%	210,700.00		-	100.00%	210,700.00	0.00%	0.00	
	SUMMARY PRELIM COST			3,512,100.00	100.00%	3,512,100.00	0%	-	100.00%	3,512,100.00	0.00%	0.00	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB

DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
	INTERIOR WORKS													
1	SEATING AREA		1.00	UNIT	19,575,757.00	89.64%	17,548,268.25	10.36%	2,027,488.75	100.00%	19,575,757.00	0.00%	-	
2	MAIN BAR AREA		1.00	UNIT	4,269,365.00	90.00%	3,842,428.50	10.00%	426,936.50	100.00%	4,269,365.00	0.00%	-	
3	LOBBY AREA + LOBBY W.C.		1.00	UNIT	3,757,224.00	87.30%	3,280,025.30	12.70%	477,198.70	100.00%	3,757,224.00	0.00%	-	
4	GREETER AREA		1.00	UNIT	1,355,787.00	89.69%	1,215,984.30	10.31%	139,802.70	100.00%	1,355,787.00	0.00%	-	
5	MAIN W.C. FOYER AREA		1.00	UNIT	701,492.00	89.35%	626,760.60	10.65%	74,731.40	100.00%	701,492.00	0.00%	-	
6	MAIN W.C. (PUBLIC AREA)		1.00	UNIT	5,214,311.00	87.43%	4,559,013.90	12.57%	655,297.10	100.00%	5,214,311.00	0.00%	-	
7	VIP 1		1.00	UNIT	5,843,263.00	90.53%	5,289,639.30	9.47%	553,623.70	100.00%	5,843,263.00	0.00%	-	
8	VIP 2		1.00	UNIT	10,722,856.00	90.31%	9,683,762.40	9.69%	1,039,093.60	100.00%	10,722,856.00	0.00%	-	
9	VIP 3		1.00	UNIT	7,914,741.00	90.18%	7,137,373.50	9.82%	777,367.50	100.00%	7,914,741.00	0.00%	-	
10	3 VIP W.C.s		1.00	UNIT	986,858.00	90.00%	888,172.20	10.00%	98,685.80	100.00%	986,858.00	0.00%	-	
11	VIP CORRIDOR AREA		1.00	UNIT	1,805,572.00	90.00%	1,625,014.80	10.00%	180,557.20	100.00%	1,805,572.00	0.00%	-	
	TOTAL COST OF INTERIOR WORKS				62,147,226.00	89.62%	55,696,443.05	10.38%	6,450,782.95	100.00%	62,147,226.00	0.00%	-	
1	SEATING AREA													
		FLOOR												
1.1	F1	VINYL (ANTI-SLIP) - (VE - BLACK VINYL FLOOR, CASA ROCCA)	455.00	sq.m.	545,090.00	90.00%	490,601.00	8.00%	54,489.00	100.00%	545,090.00	0.00%	-	INCLUDING SELF-LEVELING
1.2	F1	STEPS - FLOOR (ANTI-SLIP) - VINYL (ANTI-SLIP) (VE - BLACK VINYL FLOOR, CASA ROCCA)	1.00	Unit	129,005.00	90.00%	116,098.70	8.00%	12,906.30	100.00%	129,005.00	0.00%	-	
1.3		VINYL (ANTI-SLIP), DANCE FLOOR AREA (VE - BLACK VINYL FLOOR, CASA ROCCA)	144.00	sq.m.	172,512.00	90.00%	155,263.55	8.00%	17,248.45	100.00%	172,512.00	0.00%	-	INCLUDING SELF-LEVELING
1.4		STEEL STRUCTURE STAGE, VINYL PVC	1.00	Unit	843,043.00	90.00%	758,758.70	8.00%	84,284.30	100.00%	843,043.00	0.00%	-	ADD (INCLUDING SELF-LEVELING)
		STAIRS FINISHING+HANDRAIL							-					
1.5		STEPS - STONE EMPERADOR (VE -TILE 60X60 PC RATE 750/SQM.)	1.00	set	333,963.00	90.00%	300,566.70	10.00%	33,396.30	100.00%	333,963.00	0.00%	-	MAIN STRUCTURE AND LED STRIP LIGHT EXC (ONLY MAIN STAIRS)
1.6		LANDING - STONE EMPERADOR (VE -TILE 60X60 PC RATE 750/SQM.)	48.00	sq.m.	153,888.00	90.00%	138,499.20	10.00%	15,388.80	100.00%	153,888.00	0.00%	-	MAIN STRUCTURE EXC (ONLY MAIN STAIRS)
1.7		STAIRS HANDRAIL AND BALUSTRADE 2 FLOORS (TOP VE - THAI SUNG)	1.00	set										ONLY MAIN STAIRS PROSUM
		TOTAL COST OF FLOOR WORK			2,177,501.00	90.00%	1,959,787.85	10.00%	217,713.15	100.00%	2,177,501.00	0.00%	-	
		WALL												
1.8	CO-01 (EPA-01)	LAYERED WALL, PROWALL STRUCTURE FIRE RETARDANT BOARD BACKING, FINISHED SUBLIME PENCIL SPRAY	582.00	sq.m.	2,577,678.00	95.00%	2,448,794.10	5.00%	128,883.90	100.00%	2,577,678.00	0.00%	-	LED EXC
1.9	PA-02	PAINT COLOUR BLACK FINISH - SKIMCOAT INCLUDED	252.00	sq.m.	157,248.00	95.00%	149,385.60	5.00%	7,862.40	100.00%	157,248.00	0.00%	-	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
1.10	ST-02	PROWALL STRUCTURE WITH GREY TRAVERTINE MARBLE, POLISHED - COFFEE WOOD (CFW)	82.00	sq.m.	-									CANCELLED
1.11		STEEL STRUCTURE WITH HMR BACKING FOR LED SCREEN	1.00	set	-									EXCLUDED
		TOTAL COST OF WALL WORK			**2,734,926.00**	**95.00%**	**2,598,179.70**	**5.00%**	**136,746.30**	**100.00%**	**2,734,926.00**	**0.00%**	**-**	
		CEILING												
1.12	CL-01	GYPSUM BOARD FINISHED CEILING PAINT BLACK COLOR WITH SHADOWLINE, INCLUDING STEEL SUPPORT FOR CEILING STRUCTURE	717.00	sq.m.	2,605,578.00	95.00%	2,475,299.10	5.00%	130,278.90	100.00%	2,605,578.00	0.00%	-	CHANDELIER SUPPORT EXC
1.13		CEILING CURVED HMR FINISHED PAINT BLACK COLOR AND ALUMINIUM STRIP SKIRTING INCLUDING STEEL SUPPORT	64.00	m.	744,000.00	95.00%	706,800.00	5.00%	37,200.00	100.00%	744,000.00	0.00%	-	LED LIGHTING & SCREEN EXC
1.14		CEILING WITH FIRE RETARDANT BOARD BACKING FOR LED SCREEN INCLUDING STEEL SUPPORT	64.00	m.	407,296.00	95.00%	386,931.20	5.00%	20,364.80	100.00%	407,296.00	0.00%	-	LED REEN EXC
1.15		CEILING WITH DECORATIVE CEILING SKIRTING BLACK SPRAY FINISH INCLUDING STEEL SUPPORT	100.00	m.	5,227,000.00	95.00%	4,965,650.00	5.00%	261,350.00	100.00%	5,227,000.00	0.00%	-	LED LIGHTING EXC
		TOTAL COST OF CEILING WORK			**8,983,874.00**	**95.00%**	**8,534,680.30**	**5.00%**	**449,193.70**	**100.00%**	**8,983,874.00**	**0.00%**	**-**	
		BUILT-IN FURNITURE												
1.16	BF-01	STAGE COUNTER WITH LED LIGHTING (BACK OF SEATS)	1.00	Set	417,373.00	0.00%	-	100.00%	417,373.00	100.00%	417,373.00	0.00%	-	LED TV EXCLUDED PRINTED TILE PROSUM
1.17	BF-02	STAGE COUNTER, DJ BOOTH WITH LED LIGHTING (ON STAGE)	1.00	Set	100,851.00	0.00%	-	100.00%	100,851.00	100.00%	100,851.00	0.00%	-	LED TV EXCLUDED
1.18	BF-03	FIXED TABLE STAINLESS AND BLUE TILE 1000X1000X352, MAIN LOUNGE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	46.00	Set	656,558.00	90.00%	590,902.20	10.00%	65,655.80	100.00%	656,558.00	0.00%	-	PRINTED TILE PROSUM
1.19	BF-04	MAIN LOUNGE SEATING TYPE 2, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	2.00	Set	392,576.00	90.00%	353,318.40	10.00%	39,257.60	100.00%	392,576.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.2	BF-05	MAIN LOUNGE SEATING TYPE 3, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	2.00	Set	380,560.00	90.00%	342,504.00	10.00%	38,056.00	100.00%	380,560.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.21	BF-06	MAIN LOUNGE SEATING TYPE 4, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	2.00	Set	312,460.00	90.00%	281,214.00	10.00%	31,246.00	100.00%	312,460.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.22	BF-07	MAIN LOUNGE SEATING TYPE 5, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	4.00	Set	448,660.00	90.00%	403,794.00	10.00%	44,866.00	100.00%	448,660.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.23	BF-08	MAIN LOUNGE SEATING TYPE 6, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	2.00	Set	729,072.00	90.00%	656,164.80	10.00%	72,907.20	100.00%	729,072.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.24	BF-09	MAIN LOUNGE SEATING TYPE 7, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	2.00	Set	576,848.00	90.00%	519,163.20	10.00%	57,684.80	100.00%	576,848.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
1.25	BF-10	MAIN LOUNGE SEATING TYPE 8, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	2.00	Set	424,624.00	90.00%	382,161.60	10.00%	42,462.40	100.00%	424,624.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.26	BF-11	MAIN LOUNGE SEATING TYPE 9, TOP BLUE TILE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	2.00	Set	292,432.00	90.00%	263,188.80	10.00%	29,243.20	100.00%	292,432.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.27	BF-12	MAIN LOUNGE SEATING TYPE 10, TOP GREY MARBLE (VE-PRINTED TILE 120X120, NONE TEXTURE METAL FILM WPC)	3.00	Set	947,442.00	70.00%	663,209.40	30.00%	284,232.60	100.00%	947,442.00	0.00%	-	PRINTED TILE PROSUM (CUSHION PILLOW EXC)
1.28	BF-13	MAIN LOUNGE SEATING TYPE 11, TOP GREY MARBLE (VE-PRINTED TILE 120X120)	4.00	Set	-									ON STAGE (CANCELLED)
1.29	BF-14	MAIN LOUNGE SEATING TYPE 12, TOP GREY MARBLE (VE-PRINTED TILE 120X120)	1.00	Set	-									ON STAGE (CANCELLED)
1.30	BF-15	DECORATIVE COLUMN H. 9.7 M. STEEL STRUCTURE WITH STEEL PLATE (OFFER STAINLESS SPRAYED FINISH)	8.00	set	-									PRO SUM
		TOTAL COST OF BUILT-IN WORK			5,679,456.00	78.45%	4,455,620.40	21.55%	1,223,835.60	100.00%	5,679,456.00	0.00%	-	
		DOOR												
1.31	D3	STAINLESS SINGLE DOOR	4.00	Unit	-									BOH EXC
		TOTAL COST OF DOOR WORK			-									
		TOTAL COST OF SEATING AREA			19,575,757.00	89.64%	17,548,268.25	10.36%	2,027,488.75	100.00%	19,575,757.00	0.00%	-	
2	MAIN BAR AREA													
		FLOOR												
2.1	F2	TILE FLOOR (ANTI-SLIP) - CORONA 02 60X60 CM. (VE- STONE GREY ANTI SLI	49.00	sq.m.	136,955.00	90.00%	123,259.50	10.00%	13,695.50	100.00%	136,955.00	0.00%	-	INCLUDING SELF-LEVELING
		TOTAL COST OF FLOOR WORK			136,955.00	90.00%	123,259.50		13,695.50	100.00%	136,955.00	0.00%	-	
		CEILING												
2.2		CURVED CEILING, STEEL STRUCTURE WITH PLYWOOD FINISH STAINLESS SHEET AND METALIC PAINT (STAINLESS SPRAYED FINISH)	1.00	Set	296,980.00	90.00%	267,282.00	10.00%	29,698.00	100.00%	296,980.00	0.00%	-	
		TOTAL COST OF CEILING WORK			296,980.00	90.00%	267,282.00	10.00%	29,698.00	100.00%	296,980.00	0.00%	-	
		BUILT-IN FURNITURE												
2.3	BF-16	MAIN LOUNGE BAR COUNTER WITH LED STRIP LIGHT, COLUMN FINISH INCLUDED (HMR DECORATIVE VERTICAL LATTEN)	1.00	Set	1,573,430.00	90.00%	1,416,087.00	10.00%	157,343.00	100.00%	1,573,430.00	0.00%	-	
2.4	BF-17	CANOPY PAVILLION, STEEL STRUCTURE WITH FIRE RETARDANT BOARD BACKING AND STEEL CLADDING, SPRAYED FINISH	1.00	Set	2,262,000.00	90.00%	2,035,800.00	10.00%	226,200.00	100.00%	2,262,000.00	0.00%	-	LED SCREEN EXCLUDED
		TOTAL COST OF BUILT-IN WORK			3,835,430.00	90.00%	3,451,887.00	10.00%	383,543.00	100.00%	3,835,430.00	0.00%	-	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
		DOOR												
2.5	D4	STAINLESS SINGLE DOOR	1.00	Unit	-									BOH EXC
		TOTAL COST OF DOOR WORK			-									
		TOTAL COST OF MAIN BAR AREA			4,269,365.00	90.00%	3,842,428.50	10.00%	426,936.50	100.00%	4,269,365.00	0.00%	-	
3	LOBBY AREA + LOBBY W.C.													
		FLOOR												
3.1	F3	BLACK MARQUINA MARBLE FLOOR (POLISHED) (VE-PRINTED TILE 60X60 CM.	81.00	sq.m.	77,760.00	80.00%	62,208.00	20.00%	15,552.00	100.00%	77,760.00	0.00%	-	PRINTED TILE PRO SUM INCLUDING SELF-LEVELING
3.2	SK-02	STONE SKIRTING, BLACK MURQUINA MARBLE, POLISHED	6.00	m.	11,088.00	80.00%	8,870.40	20.00%	2,217.60	100.00%	11,088.00	0.00%	-	
3.3		WATERPROOF FOR WC	9.00	sq.m.	2,880.00	50.00%	1,440.00	50.00%	1,440.00	100.00%	2,880.00	0.00%	-	ADD (LOBBY W.C.)
3.4	F2	TILE FLOOR (ANTI-SLIP) - CORONA 02 60X60 CM. (VE- STONE GREY ANTI SLI	9.00	sq.m.	25,155.00	90.00%	22,639.50	10.00%	2,515.50	100.00%	25,155.00	0.00%	-	ADD (LOBBY W.C.)
		TOTAL COST OF FLOOR WORK			116,883.00	81.41%	95,157.90	18.59%	21,725.10	100.00%	116,883.00	0.00%	-	
		WALL												
3.5	WD-01	PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING, CNC GROOVED WOOD BOARD (VE - FLUTED WALL PANEL BAIJAX, PC RATE 1,600/SQM)	27.00	sq.m.	138,132.00	90.00%	124,318.80	10.00%	13,813.20	100.00%	138,132.00	0.00%	-	
3.6	GL-01	PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING COVERED FROSTED GLASS (VE-MIRROR WITH FLUTED STICKER)	29.00	sq.m.	236,930.00	90.00%	213,237.00	10.00%	23,693.00	100.00%	236,930.00	0.00%	-	
3.7	PA-02	PAINT COLOUR BLACK FINISH - SKIMCOAT INCLUDED	12.00	sq.m.	7,488.00	90.00%	6,739.20	10.00%	748.80	100.00%	7,488.00	0.00%	-	
3.8	DP-01	PROWALL STRUCTURE DECORATIVE PANEL, ALUMINIUM SHEET AND MOSAIC TILE PATTERN (AL-02 > METALIC PAINT, TOA)	1.00	set	208,032.00	90.00%	187,228.80	10.00%	20,803.20	100.00%	208,032.00	0.00%	-	
3.9	DP-02	PROWALL STRUCTURE DECORATIVE PANEL, ALUMINIUM SHEET AND MOSAIC TILE PATTERN (AL-02 > METALIC PAINT, TOA)	1.00	set	173,600.00	90.00%	156,240.00	10.00%	17,360.00	100.00%	173,600.00	0.00%	-	
3.10	DP-03	PROWALL STRUCTURE DECORATIVE PANEL, ALUMINIUM SHEET WITH METAL FRAME (AL-02 > METALIC PAINT, WPC ALUMINIUM SHEET)	1.00	set	83,806.00	90.00%	75,425.40	10.00%	8,380.60	100.00%	83,806.00	0.00%	-	
3.11	DP-04	DECORATIVE PANEL, WROUGHT IRON	3.00	set	93,240.00	90.00%	83,916.00	10.00%	9,324.00	100.00%	93,240.00	0.00%	-	LAB COST INCLUDED
3.12	TL-01	ARKETY GREY (1CM. THICKNESS, NATURAL SURFACE) 60X60 CM. - SKIM COAT INCLUDED (VE - STONE EMPEROR TILE THAI SUNG, PC RATE 620/SQM.)	39.00	sq.m.	103,116.00	90.00%	92,804.40	10.00%	10,311.60	100.00%	103,116.00	0.00%	-	WATERPROOF INCLUDED ADD (LOBBY W.C.)
3.13	TL-01.1	ARKETY GREY (1CM. THICKNESS, NATURAL SURFACE) 60X60 CM. DOUBLE WALL (VE - STONE EMPEROR TILE THAI SUNG, PC RATE 620/SQM.)	2.00	sq.m.	6,056.00	90.00%	5,450.40	10.00%	605.60	100.00%	6,056.00	0.00%	-	ADD (LOBBY W.C.)
3.14	GL-02.1	CLEAR MIRROR WITH PROWALL STRUCTURE AND FIRE RETARDANT BOARD E	1.00	SET	8,967.00	90.00%	8,070.30	10.00%	896.70	100.00%	8,967.00	0.00%	-	ADD (LOBBY W.C.)

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
		TOTAL COST OF WALL WORK			1,059,367.00	90.00%	953,430.30	10.00%	105,936.70	100.00%	1,059,367.00	0.00%	-	
		CEILING												
3.13	CL-04	C-LINE STRUCTURE RIPPLE EMBOSSED PATTERN ALUMINIUM SHEET VE-WPC METAL SERIES)	64.00	sq.m.	161,600.00	90.00%	145,440.00	10.00%	16,160.00	100.00%	161,600.00	0.00%	-	
3.14	CL-05	STEEL STRUCTURE WITH CLEAR MIRROR FINISH AND ALUMINIUM FRAME (SNACK BAR) (VE-TYK)	1.00	Unit	117,231.00	90.00%	105,507.90	10.00%	11,723.10	100.00%	117,231.00	0.00%	-	
3.15	CL-01.1	MOISTURE RESISTANCE GYPSUM BOARD FINISH CEILING PAINT BLACK COLOR	9.00	sq.m.	16,920.00	90.00%	15,228.00	10.00%	1,692.00	100.00%	16,920.00	0.00%	-	ADD (LOBBY W.C.)
		TOTAL COST OF CEILING WORK			295,751.00	90.00%	266,175.90	10.00%	29,575.10	100.00%	295,751.00	0.00%	-	
		BUILT-IN FURNITURE												
3.16	BF-18	LOBBY COUNTER (NO DETAILS, ACCORDING TO SKETCHUP)	1.00	Set	609,037.00	90.00%	548,133.30	10.00%	60,903.70	100.00%	609,037.00	0.00%	-	POPCORN CONTAINER AND EQUIPMENTS EXC
3.17	BF-19	HANGING SHELF, STAINLESS SHEET FINISH	1.00	Set	224,721.00	90.00%	202,248.90	10.00%	22,472.10	100.00%	224,721.00	0.00%	-	
3.18	BF-20	LOBBY CURVED SEATING WITH LED STRIP LIGHTING INCLUDED (VE - METAL FILM WPC)	1.00	Set	104,150.00	100.00%	104,150.00		-	100.00%	104,150.00	0.00%	-	
3.19	BF-21	DECORATIVE COLUMN H. 3.5 M. STEEL STRUCTURE WITH STEEL PLATE (OFFER STAINLESS SPRAYED FINISH)	6.00	set										PRO SUM
3.20	BF-22	STAINLESS SPRAYED FINISH ARCH, LOBBY	3.00	Set	132,837.00	80.00%	106,269.60	20.00%	26,567.40	100.00%	132,837.00	0.00%	-	
		TOTAL COST OF BUILT-IN WORK			1,070,745.00	89.73%	960,801.80	10.27%	109,943.20	100.00%	1,070,745.00	0.00%	-	
		DOOR												
3.21	D1	STAINLESS ARCH DOUBLE DOOR WITH FIRE INSULATION, ALUMINIUM STRIP AND FLUTED GLASS (VE-DOOR HANDLE, PC RATE 2,500/PIECE)	2.00	Unit	910,154.00	90.00%	819,138.60	10.00%	91,015.40	100.00%	910,154.00	0.00%	-	
3.22	D2	STAINLESS DOUBLE DOOR WITH FIRE INSULATION, ALUMINIUM STRIP (DOOR HANDLE, PC RATE 2,500/PIECE)	1.00	Unit	211,336.00	70.00%	147,935.20	30.00%	63,400.80	100.00%	211,336.00	0.00%	-	
3.23	D4	SINGLE DOOR	1.00	Unit	-									CHANGE TO D5 (LOBBY W.C.)
3.24	D5	TOILET SINGLE DOOR, ALUMINIUM STRIP	1.00	Unit	66,148.00	20.00%	13,229.60	80.00%	52,918.40	100.00%	66,148.00	0.00%	-	
		TOTAL COST OF DOOR WORK			1,187,638.00	82.54%	980,303.40	17.46%	207,334.60	100.00%	1,187,638.00	0.00%	-	
		SANITARY WARE												ADD (LOBBY W.C.)
3.25	SN-01	TOILET SEAT W/ BIDET FUNCTION ECO WASHER	1.00	Set	-									CANCELLED
3.26	SN-02	WALL HUNG TOILET ONLY BOWL CEF	1.00	Set	-									CANCELLED
3.27	SN-02	SPLIT-TYPE TOILET BOWL (VE-OEM SANITARY SUPPLIER)	1.00	Set	10,955.00	90.00%	9,859.50	10.00%	1,095.50	100.00%	10,955.00	0.00%	-	
3.28	SN-03	CONCEALED TOILET SENSOR FV	1.00	Set	-									CANCELLED
3.29	SN-04	FRAME	1.00	Set	-									CANCELLED

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
3.30	SN-05	RUBBER SPUD	1.00	Set	-									CANCELLED
3.31	SN-06	SLIP-IN CONNECTOR	1.00	Set	-									CANCELLED
3.32	SN-07	SUPPLY PIPE	1.00	Set	-									CANCELLED
3.33	SN-08	STOP VALVE	1.00	Set	-									CANCELLED
3.34	SN-09	TOILET PAPER HOLDER (VE-OEM SANITARY SUPPLIER)	1.00	Set	503.00	90.00%	452.70	10.00%	50.30	100.00%	503.00	0.00%	-	ADD
3.35	SN-10	WALL HUNG URINAL W/BUILT-IN SENSOR (AC) (VE-OEM SANITARY SUPPLIER)	1.00	Set	8,322.00	90.00%	7,489.80	10.00%	832.20	100.00%	8,322.00	0.00%	-	
3.36	SN-11	WALL HUNG BASIN *REPLACE MODEL (VE-OEM SANITARY SUPPLIER)	1.00	Set	7,060.00	90.00%	6,354.00	10.00%	706.00	100.00%	7,060.00	0.00%	-	
3.37	SN-12	SINGLE LEVER BASIN FAUCET W/O POP-UP WAS (VE-OEM SANITARY SUPPLIER)	1.00	Set	-									INCLUDED IN SN-11
3.38	SN-13	POP-UP WASTE FOR BASIN (VE-OEM SANITARY SUPPLIER)	1.00	Set	-									INCLUDED IN SN-11
3.39	SN-14	CONNECTOR FOR POP-UP W/TOTO P-TRAP (VE-OEM SANITARY SUPPLIER)	1.00	Set	-									INCLUDED IN SN-11
3.40	SN-15	DRAIN PIPE FOR BASIN (P-TRAP EXTRA) (VE-OEM SANITARY SUPPLIER)	1.00	Set	-									INCLUDED IN SN-11
3.41	SN-16	STOP VALVE (VE-OEM SANITARY SUPPLIER)	1.00	Set	-									INCLUDED IN SN-11
		TOTAL COST OF SANITARY WORK			26,840.00	90.00%	24,156.00	10.00%	2,684.00	100.00%	26,840.00	0.00%	-	
		TOTAL COST OF LOBBY AREA + LOBBY W.C.			3,757,224.00	87.30%	3,280,025.30	12.70%	477,198.70	100.00%	3,757,224.00	0.00%	-	
4	GREETER AREA													
		FLOOR												
4.1	F3	BLACK MARQUINA MARBLE FLOOR (POLISHED) (VE-PRINTED TILE 60X60 CM.)	44.00	sq.m.	42,240.00	80.00%	33,792.00	20.00%	8,448.00	100.00%	42,240.00	0.00%	-	PRINTED TILE PRO SUM INCLUDING SELF-LEVELING
4.2	SK-02	STONE SKIRTING, BLACK MURQUINA MARBLE, POLISHED	15.00	m.	27,720.00	90.00%	24,948.00	10.00%	2,772.00	100.00%	27,720.00	0.00%	-	
4.3		STEPS - BLACK MARQUINA MARBLE (VE-PRINTED TILE 60X60 CM.)	1.00	Unit	96,046.00	90.00%	86,441.40	10.00%	9,604.60	100.00%	96,046.00	0.00%	-	PRINTED TILE PROSUM
		TOTAL COST OF FLOOR WORK			166,006.00	87.46%	145,181.40	12.54%	20,824.60	100.00%	166,006.00	0.00%	-	
		WALL												
4.4	WD-01	PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING, CNC GROOVED WOOD BOARD (VE - FLUTED WALL PANEL BAIJAX, PC RATE 1,600/SQM)	51.00	sq.m.	260,916.00	90.00%	234,824.40	10.00%	26,091.60	100.00%	260,916.00	0.00%	-	
4.5	PA-02	PAINT COLOUR BLACK FINISH - SKIMCOAT INCLUDED	9.00	sq.m.	5,616.00	90.00%	5,054.40	10.00%	561.60	100.00%	5,616.00	0.00%	-	
4.6	DP-05	PROWALL STRUCTURE DECORATIVE PANEL, ALUMINIUM SHEET WITH METAL FRAME (VE-WPC METAL SERIES)	1.00	set	83,806.00	90.00%	75,425.40	10.00%	8,380.60	100.00%	83,806.00	0.00%	-	
		TOTAL COST OF WALL WORK			350,338.00	90.00%	315,304.20	10.00%	35,033.80	100.00%	350,338.00	0.00%	-	
		CEILING												

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
4.7	CL-04	C-LINE STRUCTURE RIPPLE EMBOSSED PATTERN ALUMINIUM SHEET VE-WPC METAL SERIES)	33.00	sq.m.	83,325.00	90.00%	74,992.50	10.00%	8,332.50	100.00%	83,325.00	0.00%	-	
4.8	CL-06	STEEL STRUCTURE, ALUMINIUM FRAME WITH PRINTED GRAPHIC FINIAH AND LED LIGHTING	1.00	Unit	108,738.00	90.00%	97,864.20	10.00%	10,873.80	100.00%	108,738.00	0.00%	-	
		TOTAL COST OF CEILING WORK			192,063.00	90.00%	172,856.70	10.00%	19,206.30	100.00%	192,063.00	0.00%	-	
		BUILT-IN FURNITURE												
4.9	BF-23	RECEPTION (NO DETAILS, ACCORDING TO SKETCHUP)	1.00	Set	647,380.00	90.00%	582,642.00	10.00%	64,738.00	100.00%	647,380.00	0.00%	-	
4.10	BF-21	DECORATIVE COLUMN H. 3.5 M. (OFFER STAINLESS SPRAYED FINISH)	3.00	set	-									PRO SUM
		TOTAL COST OF BUILT-IN WORK			647,380.00	90.00%	582,642.00	10.00%	64,738.00	100.00%	647,380.00	0.00%	-	
		DOOR												
4.11	D1	STAINLESS ARCH DOUBLE DOOR	2.00	Unit	-									INCLUDED IN LOBBY AREA
		TOTAL COST OF DOOR WORK			-									
		TOTAL COST OF GREETER AREA			1,355,787.00	89.69%	1,215,984.30	10.31%	139,802.70	100.00%	1,355,787.00	0.00%	-	
5	MAIN W.C. FOYER AREA													
		FLOOR												
5.1	F3	BLACK MARQUINA MARBLE FLOOR (POLISHED) (VE-PRINTED TILE 60X60 CM.)	44.00	sq.m.	42,240.00	80.00%	33,792.00	20.00%	8,448.00	100.00%	42,240.00	0.00%	-	PRINTED TILE PRO SUM INCLUDING SELF-LEVELING
		TOTAL COST OF FLOOR WORK			42,240.00	80.00%	33,792.00	20.00%	8,448.00	100.00%	42,240.00	0.00%	-	
		WALL												
5.2	AL-01	ALUMINIUM SHEET, WATER RIPPLE EMBOSSED PATTERN, GREEN COLOR (VE-WPC METAL SERIES, PC RATE 3,500/SHEET)	51.00	sq.m.	256,479.00	90.00%	230,831.10	10.00%	25,647.90	100.00%	256,479.00	0.00%	-	
5.3	PA-02	PAINT COLOUR BLACK FINISH - SKIMCOAT INCLUDED	27.00	sq.m.	16,848.00	90.00%	15,163.20	10.00%	1,684.80	100.00%	16,848.00	0.00%	-	
5.4	ST-01	PRO-WALL STRUCTURE WITH GREY EMPERADOR, POLISHED FINISH (According to the skp)	1.00	sq.m.	1,194.00	60.00%	716.40	40.00%	477.60	100.00%	1,194.00	0.00%	-	PRINTED TILE PROSUM (ENTRANCE)
5.5	MT-02	PRO-WALL STRUCTURE BLACK STAINLESS STEEL - ANTIQUE COPPER HL (According to the skp)	2.00	sq.m.	19,256.00	90.00%	17,330.40	10.00%	1,925.60	100.00%	19,256.00	0.00%	-	ENTRANCE
5.6	DP-06	PROWALL STRUCTURE ARCH DECORATIVE WALL PANEL, CNC PATTERN AND MOSAIC TILE METALLIC LITE GREY 30.5X31 CM.	2.00	set	142,018.00	90.00%	127,816.20	10.00%	14,201.80	100.00%	142,018.00	0.00%	-	
		TOTAL COST OF WALL WORK			435,795.00	89.92%	391,857.30	10.08%	43,937.70	100.00%	435,795.00	0.00%	-	
		CEILING												
5.7	CL-04	C-LINE STRUCTURE RIPPLE EMBOSSED PATTERN ALUMINIUM SHEET VE-WPC METAL SERIES)	8.00	sq.m.	20,200.00	90.00%	18,180.00	10.00%	2,020.00	100.00%	20,200.00	0.00%	-	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
5.8		CURVED CEILING SKIRT, DARK COLOUR SPRAY	1.00	unit	203,257.00	90.00%	182,931.30	10.00%	20,325.70	100.00%	203,257.00	0.00%	-	NO DETAIL DRAWING (According to the skp)
		TOTAL COST OF CEILING WORK			223,457.00	90.00%	201,111.30	10.00%	22,345.70	100.00%	223,457.00	0.00%	-	
		TOTAL COST OF MAIN W.C. FOYER AREA			701,492.00	89.35%	626,760.60	10.65%	74,731.40	100.00%	701,492.00	0.00%	-	
6	MAIN W.C. (PUBLIC AREA)													
		FLOOR												
6.1		WATERPROOF FOR WC	82.00	sq.m.	26,240.00	100.00%	26,240.00		-	100.00%	26,240.00	0.00%	-	
6.2	F2	TILE FLOOR (ANTI-SLIP) - CORONA 03 60X60 CM. (VE- STONE GREY ANTI SLIP TILE 60X60 CM.)	82.00	sq.m.	229,190.00	30.00%	68,757.00	70.00%	160,433.00	100.00%	229,190.00	0.00%	-	INCLUDING SELF-LEVELING
		TOTAL COST OF FLOOR WORK			255,430.00	37.19%	94,997.00	62.81%	160,433.00	100.00%	255,430.00	0.00%	-	
		WALL												
6.3		WATERPROOF FOR WC	32.00	sq.m.	10,240.00	100.00%	10,240.00		-	100.00%	10,240.00	0.00%	-	
6.4	MT-02	BLACK STAINLESS STEEL - ANTIQUE COPPER HL	-	sq.m.	-									NIC
6.5	MT-03	WALL FRAME FINISHED HAIRLINE GOLD STAINLESS STEEL - ANTIQUE BRASS HL (VE - STAINLESS SPRAYED FINISH)	14.00	SET	59,402.00	90.00%	53,461.80	10.00%	5,940.20	100.00%	59,402.00	0.00%	-	
6.6	AL-01	ALUMINIUM SHEET, WATER RIPPLE EMBOSSED PATTERN, GREEN COLOR (VE-WPC METAL SERIES)	11.00	sq.m.	55,319.00	90.00%	49,787.10	10.00%	5,531.90	100.00%	55,319.00	0.00%	-	
6.7	ST-01	GREY EMPERADOR, POLISHED	94.00	sq.m.	112,236.00	90.00%	101,012.40	10.00%	11,223.60	100.00%	112,236.00	0.00%	-	PRINTED TILE PROSUM
6.8	ST-01	GREY EMPERADOR POLISHED, DOUBLE WALL (VE-PRINTED TILE 60X60 CM.)	32.00	sq.m.	53,568.00	90.00%	48,211.20	10.00%	5,356.80	100.00%	53,568.00	0.00%	-	TOILET WALL - PRINTED TILE PRO SUM
6.9	TL-02	MOSAIC TILE, METALLIC LITE GREY 30.5X31 CM.	86.00	sq.m.	621,350.00	90.00%	559,215.00	10.00%	62,135.00	100.00%	621,350.00	0.00%	-	
6.10	TL-02	MOSAIC TILE, METALLIC LITE GREY 30.5X31 CM. WITH WIREMASH GRID	1.00	Unit	310,305.00	90.00%	279,274.50	10.00%	31,030.50	100.00%	310,305.00	0.00%	-	
6.11	TL-03	MOSAIC TILE, GREEN PATTERN GLASCERA LIMITED	74.00	sq.m.	652,754.00	90.00%	587,478.60	10.00%	65,275.40	100.00%	652,754.00	0.00%	-	
6.12	GL-02	PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING, COVERED WITH A CLEAR MIRROR FINISH AND ALUMINIUM FRAME	46.00	sq.m.	385,940.00	90.00%	347,346.00	10.00%	38,594.00	100.00%	385,940.00	0.00%	-	
6.13	GL-03	PROWALL STRUCTURE FLOATED GLASS - BBP	7.00	sq.m.	51,002.00	90.00%	45,901.80	10.00%	5,100.20	100.00%	51,002.00	0.00%	-	
6.14		STAINLESS FRAME WALL (VE - STAINLESS SPRAYED FINISH)	10.00	set	51,460.00	90.00%	46,314.00	10.00%	5,146.00	100.00%	51,460.00	0.00%	-	W.C. FEMALE
6.15		STAINLESS ARCHED ENTRANCE WALL (VE - STAINLESS SPRAYED FINISH)	3.00	set	47,169.00	90.00%	42,452.10	10.00%	4,716.90	100.00%	47,169.00	0.00%	-	MAIN W.C.
		TOTAL COST OF WALL WORK			2,410,745.00	90.04%	2,170,694.50	9.96%	240,050.50	100.00%	2,410,745.00	0.00%	-	
		CEILING												
6.16	CL-04	C-LINE STRUCTURE RIPPLE EMBOSSED PATTERN ALUMINIUM SHEET VE-WPC METAL SERIES)	81.00	sq.m.	204,525.00	90.00%	184,072.50	10.00%	20,452.50	100.00%	204,525.00	0.00%	-	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
6.17		CURVED CEILING, BLUE PAINT (MAIN W.C.)	5.00	unit	217,535.00	90.00%	195,781.50	10.00%	21,753.50	100.00%	217,535.00	0.00%	-	NO DETAIL DRAWING (According to the skp)
		TOTAL COST OF CEILING WORK			**422,060.00**	**90.00%**	**379,854.00**	10.00%	42,206.00	**100.00%**	**422,060.00**	**0.00%**	**-**	
		BUILT-IN FURNITURE												
6.18	BF-24	VANITY COUNTER 3.95x0.75M. (VE-PRINTED TILE 120X120)	1.00	Set	42,826.00	90.00%	38,543.40	10.00%	4,282.60	100.00%	42,826.00	0.00%	-	W.C. MALE PRINTED TILE PRO SUM
6.19	BF-25	VANITY COUNTER 4.45x0.60M. (VE-PRINTED TILE 120X120)	1.00	Set	47,705.00	90.00%	42,934.50	10.00%	4,770.50	100.00%	47,705.00	0.00%	-	W.C. FEMALE PRINTED TILE PRO SUM
6.20	BF-26	GLASS PARTITION, MAIN WC (VE-GLASS WITH FLUTED STICKER)	7.00	Set	69,951.00	90.00%	62,955.90	10.00%	6,995.10	100.00%	69,951.00	0.00%	-	W.C. MALE
		TOTAL COST OF BUILT-IN WORK			**160,482.00**	**90.00%**	**144,433.80**	10.00%	16,048.20	**100.00%**	**160,482.00**	**0.00%**	**-**	
		DOOR												
6.21	D5	TOILET SINGLE DOOR, ALUMINIUM STRIP	15.00	Unit	992,220.00	90.00%	892,998.00	10.00%	99,222.00	100.00%	992,220.00	0.00%	-	
		TOTAL COST OF DOOR WORK			**992,220.00**	**90.00%**	**892,998.00**	10.00%	99,222.00	**100.00%**	**992,220.00**	**0.00%**	**-**	
		SANITARY WARE												
6.22	SN-01	TOILET SEAT W/ BIDET FUNCTION ECO WASHER (VE-OEM SANITARY SUPPLIER)	14.00	Set	213,458.00	90.00%	192,112.20	10.00%	21,345.80	100.00%	213,458.00	0.00%	-	
6.23	SN-02	WALL-HUNG TOILET ONLY BOWL CEF WITH FRAME (VE-OEM SANITARY SUPPLIER)	14.00	Set	228,298.00	90.00%	205,468.20	10.00%	22,829.80	100.00%	228,298.00	0.00%	-	LAB INCLUDED IN SN-01
6.24	SN-03	CONCEALED TOILET SENSOR FV (VE-OEM SANITARY SUPPLIER)	14.00	Set	177,142.00	90.00%	159,427.80	10.00%	17,714.20	100.00%	177,142.00	0.00%	-	
6.25	SN-04	FRAME (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-02
6.26	SN-05	RUBBER SPUD (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-02
6.27	SN-06	SLIP-IN CONNECTOR (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-02
6.28	SN-07	SUPPLY PIPE (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-02
6.29	SN-08	STOP VALVE (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-02
6.30	SN-09	TOILET PAPER HOLDER (VE-OEM SANITARY SUPPLIER)	14.00	Set	7,042.00	90.00%	6,337.80	10.00%	704.20	100.00%	7,042.00	0.00%	-	ADD
6.31	SN-10	WALL HUNG URINAL W/BUILT-IN SENSOR (AC) (VE-OEM SANITARY SUPPLIER)	8.00	Set	66,576.00	90.00%	59,918.40	10.00%	6,657.60	100.00%	66,576.00	0.00%	-	
6.32	SN-11	UNDER COUNTER LAVATORY CEFIONTECT *REPLACE MODEL	14.00	Set	-									CANCELLED
6.33	SN-12	TOUCHLESS FAUCET CONSIST *REPLACE MODEL	14.00	Set	-									CANCELLED
6.34	SN-13	ROUND CORNER COUNTER BASIN 36X36X32 CM. (VE-OEM SANITARY SUPPLIER)	8.00	Set	35,680.00	90.00%	32,112.00	10.00%	3,568.00	100.00%	35,680.00	0.00%	-	ADD
6.35	SN-14	COUNTER BASIN 40X40X25 CM. (VE-OEM SANITARY SUPPLIER)	6.00	Set	26,274.00	90.00%	23,646.60	10.00%	2,627.40	100.00%	26,274.00	0.00%	-	ADD
6.36	SN-15	SENSOR PIPE FAUCET - ROSE GOLD (VE-OEM SANITARY SUPPLIER)	14.00	Set	218,904.00	90.00%	197,013.60	10.00%	21,890.40	100.00%	218,904.00	0.00%	-	ADD
6.34	SN-13	POP-UP WASTE FOR BASIN (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-13
6.35	SN-14	CONNECTOR FOR POP-UP W/TOTO P-TRAP (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-13

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
6.36	SN-15	DRAIN PIPE FOR BASIN (P-TRAP EXTRA) (VE-OEM SANITARY SUPPLIER)	14.00	Set	-									INCLUDED IN SN-13
		TOTAL COST OF SANITARY WORK			973,374.00	90.00%	876,036.60	10.00%	97,337.40	100.00%	973,374.00	0.00%	-	
		TOTAL COST OF MAIN W.C. AREA			5,214,311.00	87.43%	4,559,013.90	12.57%	655,297.10	100.00%	5,214,311.00	0.00%	-	
7	VIP 1													
		FLOOR												
7.1	F3	BLACK MARQUINA MARBLE FLOOR (POLISHED) (VE-PRINTED TILE 60X60 CM.)	39.00	sq.m.	37,440.00	90.00%	33,696.00	10.00%	3,744.00	100.00%	37,440.00	0.00%	-	PRINTED TILE PRO SUM INCLUDING SELF-LEVELING
7.2		WATERJET TILE FLOOR, PATTERN VIP 1	1.00	unit	387,601.00	90.00%	348,840.90	10.00%	38,760.10	100.00%	387,601.00	0.00%	-	
7.3	SK-02	STONE SKIRTING, BLACK MURQUINA MARBLE, POLISHED	4.00	m.	7,392.00	90.00%	6,652.80	10.00%	739.20	100.00%	7,392.00	0.00%	-	
		TOTAL COST OF FLOOR WORK			432,433.00	90.00%	389,189.70	10.00%	43,243.30	100.00%	432,433.00	0.00%	-	
		WALL												
7.4		ACOUSTIC INSULATION WALL, PROWALL WITH FRB BACKING	111.00	sq.m.	307,026.00	100.00%	307,026.00		-	100.00%	307,026.00	0.00%	-	ADD
7.5	SP-01	SPECIAL TEXTURE WALL - SKIMCOAT INCLUDED (VE-TOA BLUE LOFT)	69.00	sq.m.	93,357.00	90.00%	84,021.30	10.00%	9,335.70	100.00%	93,357.00	0.00%	-	ELEVATION 1 & 3
7.7	GL-04 (SP-01A)	AN ANTIQUE MIRROR FINISH	24.00	sq.m.	127,008.00	90.00%	114,307.20	10.00%	12,700.80	100.00%	127,008.00	0.00%	-	ELEVATION 2 ACCORDING TO PERSPECTIVE
7.6	PA-02	PAINT COLOUR BLACK FINISH - SKIMCOAT INCLUDED	25.00	sq.m.	15,600.00	90.00%	14,040.00	10.00%	1,560.00	100.00%	15,600.00	0.00%	-	
7.8	DP-07	CURVED WALL PANEL, STEEL STRUCTURE WITH WOOD FINISH, WD-02 VENEER > WD-02A, LOFT	15.00	set	357,735.00	90.00%	321,961.50	10.00%	35,773.50	100.00%	357,735.00	0.00%	-	
7.9	DP-08	ARCH DECORATIVE WALL, PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING, CNC PATTERN, SP-02 FINISH (VE-TOA METAL LOFT)	1.00	set	68,862.00	90.00%	61,975.80	10.00%	6,886.20	100.00%	68,862.00	0.00%	-	LED EXC
		TOTAL COST OF WALL WORK			969,588.00	93.17%	903,331.80	6.83%	66,256.20	100.00%	969,588.00	0.00%	-	
		CEILING												
7.8		PAINTED CEILING	119.00	sq.m.	45,696.00	90.00%	41,126.40	10.00%	4,569.60	100.00%	45,696.00	0.00%	-	
7.9		CURVED CEILING, MT-02 FINISHED METALIC PAINT (STEEL STRUCTURE SUPPORT INCLUDED)	1.00	unit	3,237,082.00	90.00%	2,913,373.80	10.00%	323,708.20	100.00%	3,237,082.00	0.00%	-	LED LIGHTING EXC
		TOTAL COST OF CEILING WORK			3,282,778.00	90.00%	2,954,500.20	10.00%	328,277.80	100.00%	3,282,778.00	0.00%	-	
		BUILT-IN FURNITURE												
7.10	BF-27	SOFA VIP 1 STAINLESS SHEET FINISH, INCLUDING LED STRIP LIGHT	1.00	Set	376,930.00	90.00%	339,237.00	10.00%	37,693.00	100.00%	376,930.00	0.00%	-	CUSHION PILLOW EXC
7.11	BF-28	FIXED TABLE BLUE TILE, GLASS BALL AND LED STRIP LIGHTING 1200X1200X600 (VE-PRINTED TILE 120X120)	3.00	Set	298,731.00	90.00%	268,857.90	10.00%	29,873.10	100.00%	298,731.00	0.00%	-	PRINTED TILE PROSUM
7.12	BF-29	CABINET INCLUDING BASE SPRAY FINISH	1.00	Set	50,846.00	90.00%	45,761.40	10.00%	5,084.60	100.00%	50,846.00	0.00%	-	
		TOTAL COST OF BUILT-IN WORK			726,507.00	90.00%	653,856.30	10.00%	72,650.70	100.00%	726,507.00	0.00%	-	
		DOOR												

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
7.13	D9	STAINLESS SINGLE DOOR WITH FIRE INSULATION (DOOR HANDLE, PC RATE 2,500/PIECE)	1.00	Unit	83,878.00	90.00%	75,490.20	10.00%	8,387.80	100.00%	83,878.00	0.00%	-	
7.14	W1	GL-07 CLEAR GLASS WITH SOUNDPROOF FILM WINDOW (DIMENSION ACCORDING TO FLOOR PLAN) (VE-TYK)	1.00	Unit	348,079.00	90.00%	313,271.10	10.00%	34,807.90	100.00%	348,079.00	0.00%	-	HINGED WINDOW
		TOTAL COST OF DOOR WORK			431,957.00	90.00%	388,761.30	10.00%	43,195.70	100.00%	431,957.00	0.00%	-	
		TOTAL COST OF VIP 1 AREA			5,843,263.00	90.53%	5,289,639.30	9.47%	553,623.70	100.00%	5,843,263.00	0.00%	-	
8	VIP 2													
		FLOOR												
8.1	F6	ROSSO LEVANTO STONE, (VE-RUBY MARBLE RED POLISHED TILE 60X60 CM.)	120.00	sq.m.	225,360.00	90.00%	202,824.00	10.00%	22,536.00	100.00%	225,360.00	0.00%	-	ADD (Self-leveling Included)
8.2		FLOOR TILE, PATTERN VIP 2	1.00	unit	114,492.00	90.00%	103,042.80	10.00%	11,449.20	100.00%	114,492.00	0.00%	-	PRINTED TILE MAT PRO SUM
8.3	SK-02	STONE SKIRTING, BLACK MURQUINA MARBLE, POLISHED	35.00	m.	64,680.00	90.00%	58,212.00	10.00%	6,468.00	100.00%	64,680.00	0.00%	-	
		TOTAL COST OF FLOOR WORK			404,532.00	90.00%	364,078.80	10.00%	40,453.20	100.00%	404,532.00	0.00%	-	
		WALL												
8.4		ACOUSTIC INSULATION WALL, PROWALL WITH FRB BACKING	120.00	sq.m.	331,920.00	100.00%	331,920.00	0.00%	-	100.00%	331,920.00	0.00%	-	ADD
8.5	TL-03	MOSAIC TILE, GREEN PATTERN GLASCERA LIMITED	33.00	sq.m.	291,093.00	90.00%	261,983.70	10.00%	29,109.30	100.00%	291,093.00	0.00%	-	
8.6	GL-02	PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING, COVERED WITH A CLEAR MIRROR FINISH AND ALUMINIUM FRAME	6.00	sq.m.	50,340.00	90.00%	45,306.00	10.00%	5,034.00	100.00%	50,340.00	0.00%	-	
8.7	GL-04	PROWALL STRUCTURE WITH ACOUSTIC INSULATION & FIRE RETARDANT BOARD BACKING, COVERED WITH AN ANTIQUE MIRROR FINISH	36.00	sq.m.	323,928.00	90.00%	291,535.20	10.00%	32,392.80	100.00%	323,928.00	0.00%	-	ELEVATION 1,3 ACCORDING TO PERPECTIVE
8.8	GL-04 (SP-02B)	AN ANTIQUE MIRROR FINISH	59.00	sq.m.	312,228.00	90.00%	281,005.20	10.00%	31,222.80	100.00%	312,228.00	0.00%	-	ELEVATION 2,4 ACCORDING TO PERPECTIVE
8.10	PA-02	PAINT COLOUR BLACK FINISH - SKIMCOAT AND SCAFFOLDING INCLUDED	25.00	sq.m.	20,400.00	90.00%	18,360.00	10.00%	2,040.00	100.00%	20,400.00	0.00%	-	
8.11	DP-09	ARCH DECORATIVE WALL, WROUGHT IRON PATTERN 1 (2.2*3.8M.)	6.00	set	632,046.00	90.00%	568,841.40	10.00%	63,204.60	100.00%	632,046.00	0.00%	-	LAB COST INC
8.12	DP-10	ARCH DECORATIVE WALL, WROUGHT IRON PATTERN 2 (1.6*4.6M.)	6.00	set	564,480.00	90.00%	508,032.00	10.00%	56,448.00	100.00%	564,480.00	0.00%	-	LAB COST INC
8.13	DP-11	ARCH DECORATIVE WALL, WROUGHT IRON PATTERN 3	2.00	set	394,046.00	90.00%	354,641.40	10.00%	39,404.60	100.00%	394,046.00	0.00%	-	LAB COST INC
8.14	DP-12	ARCH DECORATIVE WALL, WROUGHT IRON PATTERN 4	1.00	set	184,936.00	90.00%	166,442.40	10.00%	18,493.60	100.00%	184,936.00	0.00%	-	LAB COST INC
8.15	DP-13	ARCH DECORATIVE WALL, METAL FRAME	4.00	set	197,556.00	90.00%	177,800.40	10.00%	19,755.60	100.00%	197,556.00	0.00%	-	
8.16	DP-14	STAINLESS ARCHED ENTRANCE WALL	2.00	set	91,708.00	90.00%	82,537.20	10.00%	9,170.80	100.00%	91,708.00	0.00%	-	
		TOTAL COST OF WALL WORK			3,394,681.00	90.98%	3,088,404.90		306,276.10	100.00%	3,394,681.00	0.00%	-	
		CEILING												
8.15		CEILING SPECIAL PAINT (VE - TOA WALTEX)	177.00	sq.m.	295,590.00	90.00%	266,031.00	10.00%	29,559.00	100.00%	295,590.00	0.00%	-	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
8.16		PATTERN CEILING, INCLUDING STRUCTURE SUPPORT FINISHED WD-03 AND SPRAY (WD-03 SPRAY FINISHED CANCELLED)	1.00	unit	3,939,579.00	90.00%	3,545,621.10	10.00%	393,957.90	100.00%	3,939,579.00	0.00%	-	LED LIGHTING EXC
		TOTAL COST OF CEILING WORK			4,235,169.00	90.00%	3,811,652.10	10.00%	423,516.90	100.00%	4,235,169.00	0.00%	-	
		BUILT-IN FURNITURE												
8.17	BF-28	FIXED TABLE BLUE TILE, GLASS BALL AND LED LIGHTING 1200X1200X600 (VE-PRINTED TILE 120X120)	4.00	Set	398,308.00	90.00%	358,477.20	10.00%	39,830.80	100.00%	398,308.00	0.00%	-	PRINTED TILE PROSUM
8.18	BF-30	SOFA VIP 2, WITH STAINLESS SHEET FINISH SHELF INCLUDING LED STRIP LIGHT	1.00	Set	391,335.00	90.00%	352,201.50	10.00%	39,133.50	100.00%	391,335.00	0.00%	-	CUSHION PILLOW EXC
8.19	BF-31	CABINET 1 GREY EMPERADOR FINISH, WITH STAINLESS ARCH WALL (VE-PRINTED TILE 120x120 CM.)	2.00	Set	287,238.00	90.00%	258,514.20	10.00%	28,723.80	100.00%	287,238.00	0.00%	-	PRINTED TILE PROSUM
8.20	BF-32	CABINET 2 GREY EMPERADOR FINISH, WITH STAINLESS ARCH WALL (VE-PRINTED TILE 120x120 CM.)	2.00	Set	367,972.00	90.00%	331,174.80	10.00%	36,797.20	100.00%	367,972.00	0.00%	-	PRINTED TILE PROSUM (WINE SHELF EXC)
		TOTAL COST OF BUILT-IN WORK			1,444,853.00	90.00%	1,300,367.70	10.00%	144,485.30	100.00%	1,444,853.00	0.00%	-	
		DOOR												
8.21	D10	STAINLESS DOUBLE DOOR WITH FIRE INSULATION, (2HR FIRERATE DOOR) (DOOR HANDLE, PC RATE 2,500/PIECE)	1.00	Unit	219,681.00	90.00%	197,712.90	10.00%	21,968.10	100.00%	219,681.00	0.00%	-	
8.22	W2	GL-07 SLIDING CLEAR GLASS WITH SOUNDPROOF FILM WINDOW (DIMENSION ACCORDING TO FLOOR PLAN) (VE-TYK)	1.00	Unit	1,023,940.00	90.00%	921,546.00	10.00%	102,394.00	100.00%	1,023,940.00	0.00%	-	HINGED WINDOW
		TOTAL COST OF DOOR WORK			1,243,621.00	90.00%	1,119,258.90	10.00%	124,362.10	100.00%	1,243,621.00	0.00%	-	
		TOTAL COST OF VIP 2 AREA			10,722,856.00	90.31%	9,683,762.40	9.69%	1,039,093.60	100.00%	10,722,856.00	0.00%	-	
9	VIP 3													
		FLOOR												
9.1	F3	BLACK MARQUINA MARBLE FLOOR (POLISHED) (VE-PRINTED TILE 60X60 CM.)	35.00	sq.m.	33,600.00	90.00%	30,240.00	10.00%	3,360.00	100.00%	33,600.00	0.00%	-	PRINTED TILE PRO SUM INCLUDING SELF-LEVELING
9.2		WATERJET TILE FLOOR, PATTERN VIP 3	1.00	unit	430,904.00	90.00%	387,813.60	10.00%	43,090.40	100.00%	430,904.00	0.00%	-	
9.3	SK-02	STONE SKIRTING, BLACK MURQUINA MARBLE, POLISHED	25.00	m.	46,200.00	90.00%	41,580.00	10.00%	4,620.00	100.00%	46,200.00	0.00%	-	
		TOTAL COST OF FLOOR WORK			510,704.00	90.00%	459,633.60	10.00%	51,070.40	100.00%	510,704.00	0.00%	-	
		WALL												
9.4		ACOUSTIC INSULATION WALL, PROWALL WITH FRB BACKING	51.00	sq.m.	141,066.00	100.00%	141,066.00	0.00%	-	100.00%	141,066.00	0.00%	-	ADD
9.5	GL-04	PROWALL STRUCTURE WITH ACOUSTIC INSULATION & FIRE RETARDANT BOARD BACKING, COVERED WITH AN ANTIQUE MIRROR FINISH	60.00	sq.m.	539,880.00	90.00%	485,892.00	10.00%	53,988.00	100.00%	539,880.00	0.00%	-	ACCORDING TO PERSPECTIVE

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
9.6	PA-02	PAINT COLOUR BLACK FINISH - SKIMCOAT AND SCAFFOLDING INCLUDED	5.00	sq.m.	4,080.00	90.00%	3,672.00	10.00%	408.00	100.00%	4,080.00	0.00%	-	
9.7	TL-03	MOSAIC TILE, GREEN PATTERN GLASCERA LIMITED	46.00	sq.m.	405,766.00	90.00%	365,189.40	10.00%	40,576.60	100.00%	405,766.00	0.00%	-	
9.8	SP-02A	SPECIAL PAINT (VE-PRINTED STRETCHED FABRIC)	151.00	sq.m.	398,640.00	90.00%	358,776.00	10.00%	39,864.00	100.00%	398,640.00	0.00%	-	ELEVATION 1,3
9.9	DP-15	PROWALL STRUCTURE ARCH DECORATIVE WALL, CNC PATTERN, WD-02 VENEER	1.00	set	77,676.00	90.00%	69,908.40	10.00%	7,767.60	100.00%	77,676.00	0.00%	-	
9.10	DP-09	ARCH DECORATIVE WALL, WROUGHT IRON PATTERN 1 (2.8*4.8M.)	4.00	set	719,712.00	90.00%	647,740.80	10.00%	71,971.20	100.00%	719,712.00	0.00%	-	LAB COST INC
9.11	DP-10	ARCH DECORATIVE WALL, WROUGHT IRON PATTERN 2 (1.6*4.6M.)	6.00	set	564,480.00	90.00%	508,032.00	10.00%	56,448.00	100.00%	564,480.00	0.00%	-	LAB COST INC
9.12	DP-16	ARCH DECORATIVE WALL, WROUGHT IRON PATTERN 5	1.00	set	175,477.00	90.00%	157,929.30	10.00%	17,547.70	100.00%	175,477.00	0.00%	-	LAB COST INC
		TOTAL COST OF WALL WORK			3,026,777.00	90.47%	2,738,205.90	9.53%	288,571.10	100.00%	3,026,777.00	0.00%	-	
		CEILING												
9.11		CURVED CEILING, MT-02 FINISHED COPPER SPRAY AND SPECIAL PAINT	1.00	unit	2,856,273.00	90.00%	2,570,645.70	10.00%	285,627.30	100.00%	2,856,273.00	0.00%	-	LED LIGHTING EXC
9.12		CEILING SPECIAL PAINT INCLUDE SCAFFOLDING	99.00	sq.m.	294,624.00	90.00%	265,161.60	10.00%	29,462.40	100.00%	294,624.00	0.00%	-	
		TOTAL COST OF CEILING WORK			3,150,897.00	90.00%	2,835,807.30	10.00%	315,089.70	100.00%	3,150,897.00	0.00%	-	
		BUILT-IN FURNITURE												
9.13	BF-33	SOFA VIP 3 STAINLESS FINISH, INCLUDING LED STRIP LIGHT	1.00	Set	376,930.00	90.00%	339,237.00	10.00%	37,693.00	100.00%	376,930.00	0.00%	-	CUSHION PILLOW EXC
9.14	BF-28	FIXED TABLE BLUE TILE, GLASS BALL AND LED STRIP LIGHTING 1200X1200X600 (VE-PRINTED TILE 120X120,)	3.00	Set	298,731.00	90.00%	268,857.90	10.00%	29,873.10	100.00%	298,731.00	0.00%	-	PRINTED TILE PROSUM
9.15	BF-29	CABINET VIP 3	1.00	Set	50,846.00	90.00%	45,761.40	10.00%	5,084.60	100.00%	50,846.00	0.00%	-	
9.16	BF-35	BASE VIP 3	3.00	Set	67,899.00	90.00%	61,109.10	10.00%	6,789.90	100.00%	67,899.00	0.00%	-	
		TOTAL COST OF BUILT-IN WORK			794,406.00	90.00%	714,965.40	10.00%	79,440.60	100.00%	794,406.00	0.00%	-	
		DOOR												
9.17	D9	STAINLESS SINGLE DOOR WITH FIRE INSULATION (DOOR HANDLE, PC RATE 2,500/PIECE)	1.00	Unit	83,878.00	90.00%	75,490.20	10.00%	8,387.80	100.00%	83,878.00	0.00%	-	
9.18	W1	GLASS WINDOW 180x300 CM. (DIMENSION ACCORDING TO FLOOR PLAN) (VE-TYK)	1.00	Unit	348,079.00	90.00%	313,271.10	10.00%	34,807.90	100.00%	348,079.00	0.00%	-	
		TOTAL COST OF DOOR WORK			431,957.00	90.00%	388,761.30	10.00%	43,195.70	100.00%	431,957.00	0.00%	-	
		TOTAL COST OF VIP 3 AREA			7,914,741.00	90.18%	7,137,373.50	9.82%	777,367.50	100.00%	7,914,741.00	0.00%	-	
10	3 VIP W.C.s													
		FLOOR												
10.1		WATERPROOF FOR WC	19.00	sq.m.	6,080.00	90.00%	5,472.00	10.00%	608.00	100.00%	6,080.00	0.00%	-	
10.2	F3	BLACK MARQUINA MARBLE FLOOR (POLISHED) (VE-PRINTED TILE 60X60 CM.)	19.00	sq.m.	18,240.00	90.00%	16,416.00	10.00%	1,824.00	100.00%	18,240.00	0.00%	-	PRINTED TILE PRO SUM INCLUDING SELF-LEVELING
		TOTAL COST OF FLOOR WORK			24,320.00	90.00%	21,888.00	10.00%	2,432.00	100.00%	24,320.00	0.00%	-	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
		WALL												
10.3	GL-02	CLEAR MIRROR WITH ALUMINIUM FRAME	-	sq.m.	-									INCLUDED IN BF-36
10.4	TL-01	ARKETY GREY (1CM. THICKNESS, NATURAL SURFACE) 60X60 CM. (VE - STONE EMPEROR TILE THAI SUNG, PC RATE 620/SQM.)	101.00	sq.m.	267,044.00	90.00%	240,339.60	10.00%	26,704.40	100.00%	267,044.00	0.00%	-	WATERPROOF INCLUDED
10.5	TL-03	MOSAIC TILE, GREEN PATTERN GLASCERA LIMITED	5.00	sq.m.	44,105.00	90.00%	39,694.50	10.00%	4,410.50	100.00%	44,105.00	0.00%	-	WATERPROOF INCLUDED
		TOTAL COST OF WALL WORK			311,149.00	90.00%	280,034.10	10.00%	31,114.90	100.00%	311,149.00	0.00%	-	
		CEILING												
		RECESSED CEILING	12.00	m.	14,616.00	90.00%	13,154.40	10.00%	1,461.60	100.00%	14,616.00	0.00%	-	LED STRIP LIGHT EXC
10.6	CL-04	C-LINE STRUCTURE RIPPLE EMBOSSED PATTERN ALUMINIUM SHEET VE-WPC METAL SERIES)	19.00	sq.m.	47,975.00	90.00%	43,177.50	10.00%	4,797.50	100.00%	47,975.00	0.00%	-	
		TOTAL COST OF CEILING WORK			62,591.00	90.00%	56,331.90	10.00%	6,259.10	100.00%	62,591.00	0.00%	-	
		BUILT-IN FURNITURE												
10.7	BF-36	VANITY COUNTER VIP, BLUE TILE AND PATTERNED GLASS WITH MIRROR AND LED (VE-PRINTED TILE 120X120) (VE-TYK)	3.00	Set	132,624.00	90.00%	119,361.60	10.00%	13,262.40	100.00%	132,624.00	0.00%	-	PRINTED TILE PROSUM
		TOTAL COST OF BUILT-IN WORK			132,624.00	90.00%	119,361.60	10.00%	13,262.40	100.00%	132,624.00	0.00%	-	
		DOOR												
10.9	D9	STAINLESS SINGLE DOOR WITH FIRE INSULATION (DOOR HANDLE, PC RATE 2,500/PIECE)	3.00	Unit	251,634.00	90.00%	226,470.60	10.00%	25,163.40	100.00%	251,634.00	0.00%	-	
		TOTAL COST OF DOOR WORK			251,634.00	90.00%	226,470.60	10.00%	25,163.40	100.00%	251,634.00	0.00%	-	
		SANITARY WARE												
10.10	SN-01	FULLY AUTOMATIC WC NEORESTAS COSI SOF (VE-OEM SANITARY SUPPLIER)	3.00	Set	133,887.00	90.00%	120,498.30	10.00%	13,388.70	100.00%	133,887.00	0.00%	-	
10.11	SN-02	WALL HUNG URINAL W/BUILT-IN SENSOR (AC) (VE-OEM SANITARY SUPPLIER)	3.00	Set	24,966.00	90.00%	22,469.40	10.00%	2,496.60	100.00%	24,966.00	0.00%	-	
10.12	SN-03	TOILET PAPER HOLDER (VE-OEM SANITARY SUPPLIER)	3.00	Set	1,509.00	90.00%	1,358.10	10.00%	150.90	100.00%	1,509.00	0.00%	-	ADD
10.13	SN-04	UNDER COUNTER LAVATORY CEFIONTECT *REPLACE MODEL (VE-OEM SANITARY SUPPLIER)	3.00	Set	16,746.00	90.00%	15,071.40	10.00%	1,674.60	100.00%	16,746.00	0.00%	-	
10.14	SN-05	TOUCHLESS FAUCET CONSIST *REPLACE MODEL (VE-OEM SANITARY SUPPLIER)	3.00	Set	27,432.00	90.00%	24,688.80	10.00%	2,743.20	100.00%	27,432.00	0.00%	-	
10.15	SN-06	POP-UP WASTE FOR BASIN	3.00	Set	-									INCLUDED IN SN-04
10.16	SN-07	CONNECTOR FOR POP-UP W/TOTO P-TRAP	3.00	Set	-									INCLUDED IN SN-04
10.17	SN-08	DRAIN PIPE FOR BASIN (P-TRAP EXTRA)	3.00	Set	-									INCLUDED IN SN-04
		TOTAL COST OF SANITARY WORK			204,540.00	90.00%	184,086.00	10.00%	20,454.00	100.00%	204,540.00	0.00%	-	
		TOTAL COST OF VIP W.C. AREA			986,858.00	90.00%	888,172.20	10.00%	98,685.80	100.00%	986,858.00	0.00%	-	

Progress Claim 09

PROJECT : ATLAS SUPER CLUB

DATE : 12/2/2026

SUBJECT : INTERIOR (WITH FRB WALL)

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	CODE	DESCRIPTION	QTY	UNIT	TOTAL AMOUNT	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARKS
						%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
11	VIP CORRIDOR AREA													
		FLOOR												
11.1	F3	BLACK MARQUINA MARBLE FLOOR (POLISHED) (VE-PRINTED TILE 60X60 CM.)	40.00	sq.m.	38,400.00	90.00%	34,560.00	10.00%	3,840.00	100.00%	38,400.00	0.00%	-	PRINTED TILE PRO SUM INCLUDING SELF-LEVELING
11.2	SK-02	STONE SKIRTING, BLACK MURQUINA MARBLE, POLISHED	34.00	m.	62,832.00	90.00%	56,548.80	10.00%	6,283.20	100.00%	62,832.00	0.00%	-	
		TOTAL COST OF FLOOR WORK			101,232.00	90.00%	91,108.80	10.00%	10,123.20	100.00%	101,232.00	0.00%	-	
		WALL												
11.3	GL-05	PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING, COVERED WITH AN ANTIQUE MIRROR FINISH (VE - WPC FILM FINISH)	166.00	sq.m.	768,580.00	90.00%	691,722.00	10.00%	76,858.00	100.00%	768,580.00	0.00%	-	
11.4	TL-04	PATTERN TILE, VIP CORRIDOR (PROWALL STRUCTURE WITH FIRE RETARDANT BOARD BACKING, CNC FINISHED WITH METALIC BLACK PAINT)	96.00	sq.m.	739,680.00	90.00%	665,712.00	10.00%	73,968.00	100.00%	739,680.00	0.00%	-	ADD (ACCORDING TO DESIGNER)
		TOTAL COST OF WALL WORK			1,508,260.00	90.00%	1,357,434.00	10.00%	150,826.00	100.00%	1,508,260.00	0.00%	-	
		CEILING												
11.5		STEEL STRUCTURE CEILING WITH SPECIAL PAINT FINISH INCLUDE SCAFFOLDING	40.00	sq.m.	121,680.00	90.00%	109,512.00	10.00%	12,168.00	100.00%	121,680.00	0.00%	-	NO SPEC (OFFER SPECIAL PAINT)
		TOTAL COST OF CEILING WORK			121,680.00	90.00%	109,512.00	10.00%	12,168.00	100.00%	121,680.00	0.00%	-	
		SIGNAGE												
11.6		W SUPER CLUB LOGO AT VIP CORRIDOR	1.00	Set	74,400.00	90.00%	66,960.00	10.00%	7,440.00	100.00%	74,400.00	0.00%	-	
		TOTAL COST OF SIGNAGE WORK			74,400.00	90.00%	66,960.00	10.00%	7,440.00	100.00%	74,400.00	0.00%	-	
		DOOR												
11.7														BOH EXC
		TOTAL COST OF DOOR WORK			-									
		TOTAL COST OF VIP CORRIDOR AREA			1,805,572.00	90.00%	1,625,014.80	10.00%	180,557.20	100.00%	1,805,572.00	0.00%	-	

PROJECT : ATLAS SUPER CLUB

SUBJECT : INTERIOR

DATE : 12/2/2026

BIDDER : BANGKOK DEC-CON PUBLIC COMPANY LIMITED

ITEM	DESCRIPTION	QUANTITY	UNIT	TOTAL	Previous Claimed		Claim this month		Comalative to date		Remaining value		REMARK
					%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	%	AMOUNT (BAHT)	
	PROVISIONAL SUM												
1.0	PRO-SUM STONE TILE												
1.1	BLACK TILE 60X60 CM.	1	LS.	255,552.00	90.00%	229,996.80	10.00%	25,555.20	100.00%	255,552.00	0.00%	-	F3 FLOOR
1.2	GREY TILE 120X120 CM.	1	LS.	400,791.60	90.00%	360,712.44	10.00%	40,079.16	100.00%	400,791.60	0.00%	-	BUILT IN FURNITURE & TILE WALL
1.3	BLUE TILE 120X120 CM.	1	LS.	150,836.40	90.00%	135,752.76	10.00%	15,083.64	100.00%	150,836.40	0.00%	-	BUILT-IN FURNITURE
	TOTAL COST OF PRO-SUM STONE TILE			807,180.00	90.00%	726,462.00	10.00%	80,718.00	100.00%	807,180.00	0.00%	-	
2.0	PRO-SUM DECORATIVE COLUMN												
2.1	DECORATIVE COLUMN H. 9.7 M. STEEL STRUCTURE WITH STEEL PLATE (OFFER STAINLESS SPRAYED FINISH)	1	LS.	3,899,416.00	40.00%	3,509,474.40	10.00%	389,941.60	100.00%	3,899,416.00	0.00%	-	
2.2	DECORATIVE COLUMN H. 3.0 M. STEEL STRUCTURE WITH STEEL PLATE (OFFER STAINLESS SPRAYED FINISH)	1	LS.	2,010,231.00	90.00%	1,809,207.90	10.00%	201,023.10	100.00%	2,010,231.00	0.00%	-	ADD QTY (GREETER AREA)
	TOTAL COST OF PRO-SUM DECORATIVE COLUMN			5,909,647.00	90.00%	5,318,682.30	10.00%	590,964.70	100.00%	5,909,647.00	0.00%	-	
3.0	PRO-SUM RAILING/BALUSTRADE												
3.1	STAIRS HANDRAIL AND BALUSTRADE 2 FLOORS (TOP VE - THAI SUNG)	1	UNIT	1,103,871.00	90.00%	993,483.90	10.00%	110,387.10	100.00%	1,103,871.00	0.00%	-	TOP INCLUDED
	TOTAL COST OF PRO-SUM RAILING/BALUSTRADE			1,103,871.00	90.00%	993,483.90	10.00%	110,387.10	100.00%	1,103,871.00	0.00%	-	
	SUMMARY PRELIM COST			7,820,698.00	90.00%	7,038,628.20	10.00%	782,069.80	100.00%	7,820,698.00	0.00%	-	

SECTION

1. S-Curve

BANGKOK DEC-CON
Public Company Limited

PROJECT	**:**	**ATLAS SUPERCLUB**
OWNER	**:**	**HW Group / Ratchada Entertainment**
CONSULTANT	**:**	**CMP Management Asia Co.,Ltd.**
CONTRACTOR	**:**	**Bangkok Dec-Con Public Company Limited**

BANGKOK DEC-CON
Public Company Limited

Work progress S-curve

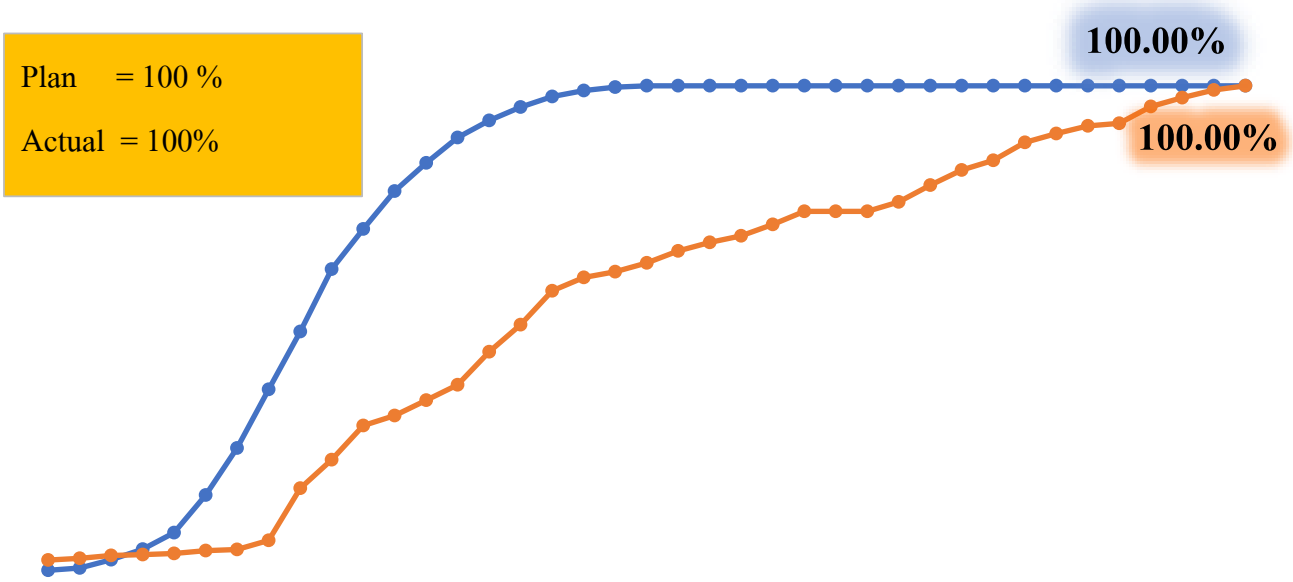

SECTION

2. Advancement Photos

BANGKOK DEC-CON
Public Company Limited

PROJECT	**:**	**ATLAS SUPERCLUB**
OWNER	**:**	**HW Group / Ratchada Entertainment**
CONSULTANT	**:**	**CMP Management Asia Co.,Ltd.**
CONTRACTOR	**:**	**Bangkok Dec-Con Public Company Limited**

BANGKOK DEC-CON
Public Company Limited

บริษัท บางกอก เดค-คอน จำกัด (มหาชน)
0-2925-5777 0-2925-5778
Admin@bangkokdeccon.com
www.bangkokdeccon.com

Photos of Completed Work

BANGKOK DEC-CON
Public Company Limited

บริษัท บางกอก เดค-คอน จำกัด (มหาชน)
0-2925-5777 0-2925-5778
Admin@bangkokdeccon.com
www.bangkokdeccon.com

Photos of Completed Work

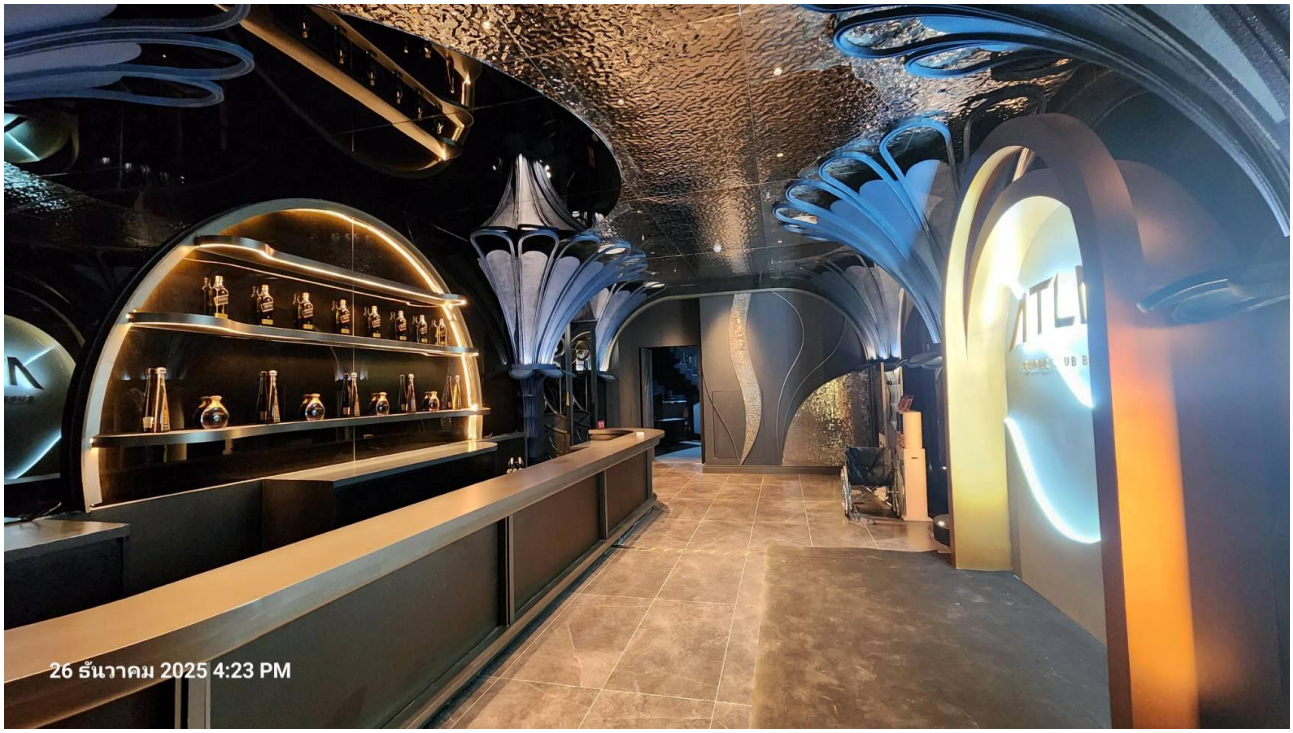

BANGKOK DEC-CON
Public Company Limited

บริษัท บางกอก เดค-คอน จำกัด (มหาชน)
0-2925-5777 0-2925-5778
Admin@bangkokdeccon.com
www.bangkokdeccon.com

Photos of Completed Work

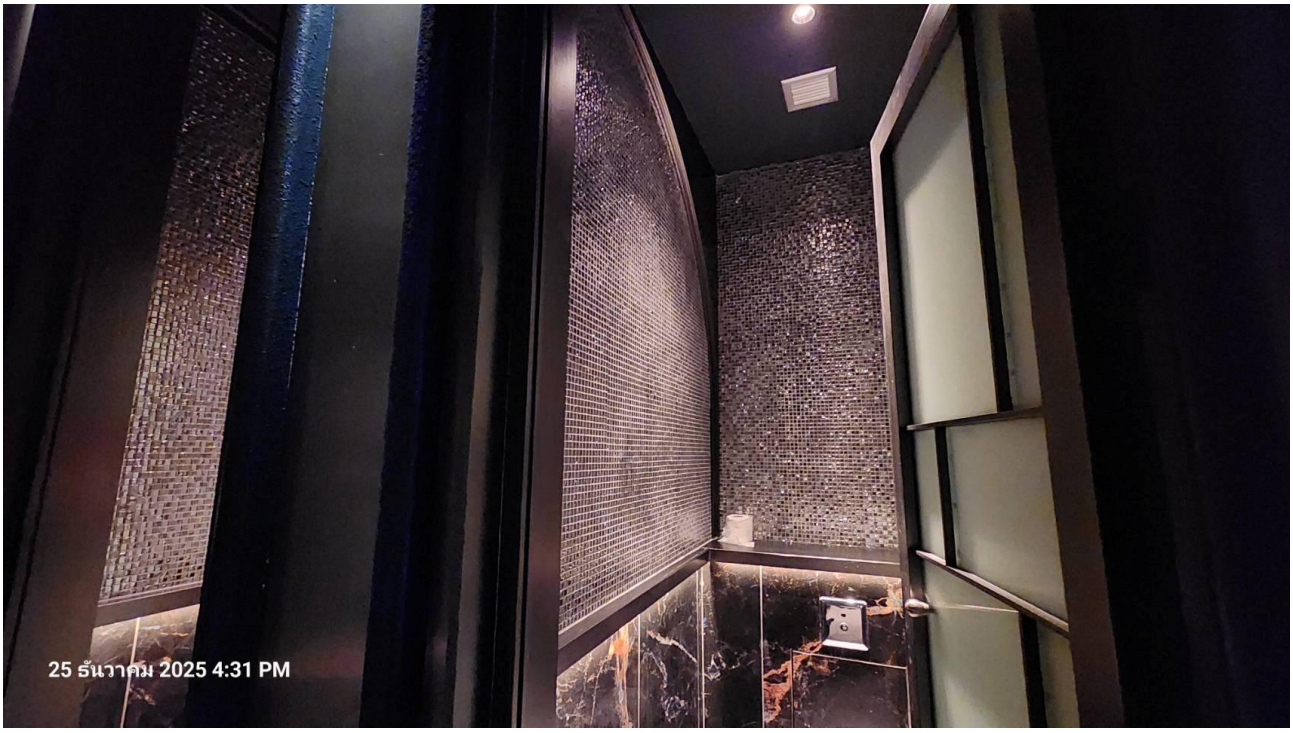

บริษัท บางกอก เดค-คอน จำกัด (มหาชน)
0-2925-5777 0-2925-5778
Admin@bangkokdeccon.com
www.bangkokdeccon.com

Photos of Completed Work

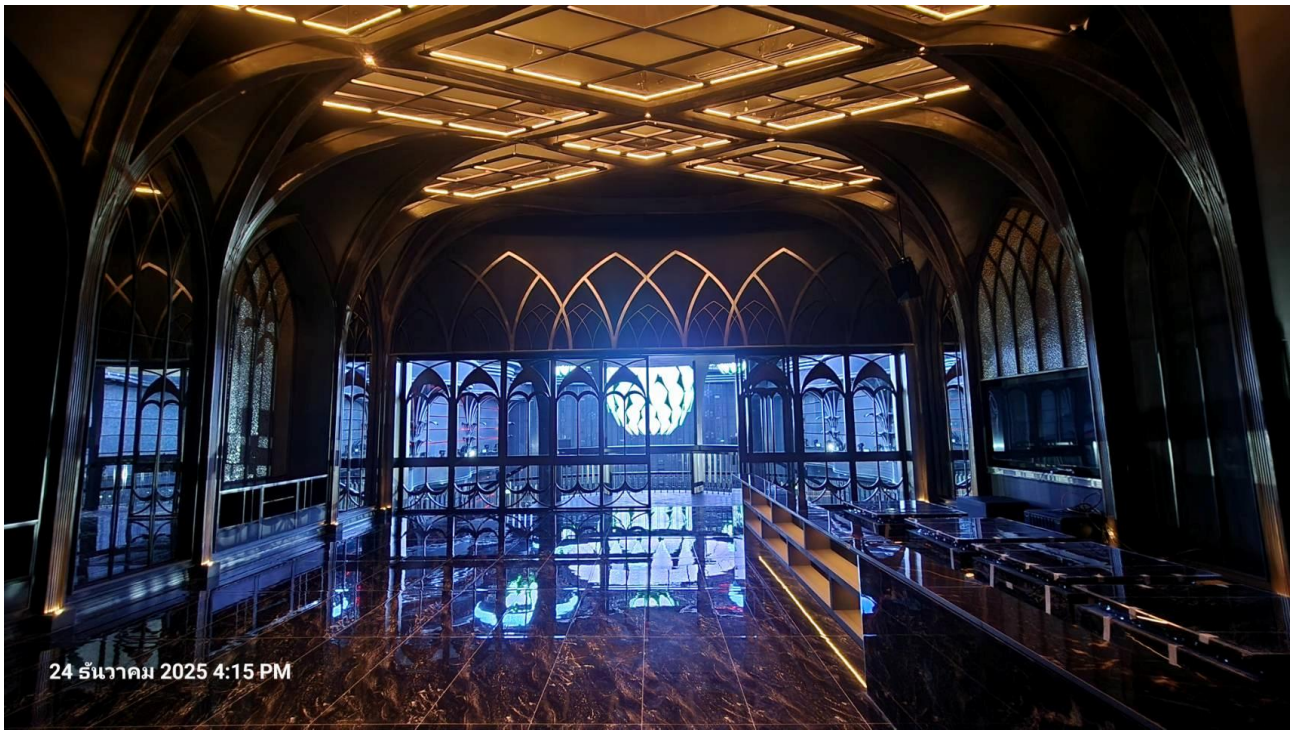

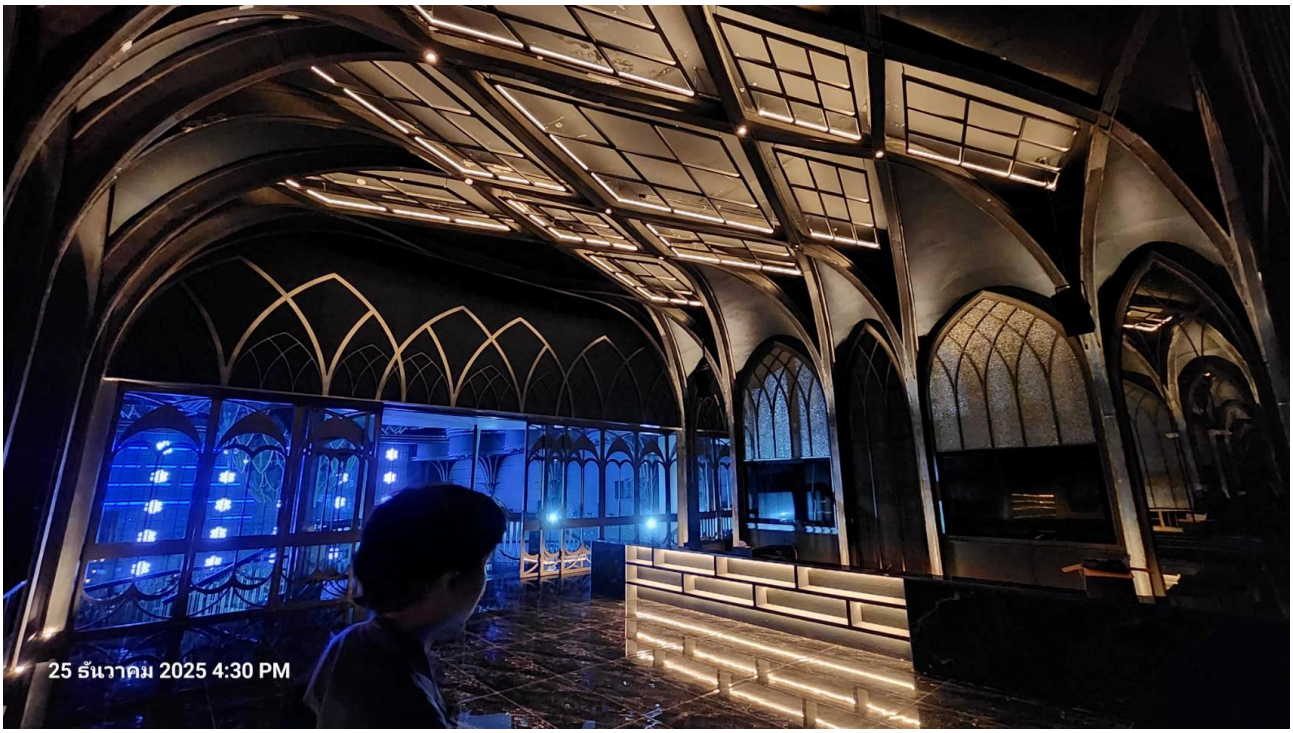

BANGKOK DEC-CON
Public Company Limited

บริษัท บางกอก เดค-คอน จำกัด (มหาชน)
0-2925-5777 0-2925-5778
Admin@bangkokdeccon.com
www.bangkokdeccon.com

Photos of Completed Work

บริษัท บางกอก เดค-คอน จำกัด (มหาชน)
0-2925-5777 0-2925-5778
Admin@bangkokdeccon.com
www.bangkokdeccon.com

Photos of Completed Work

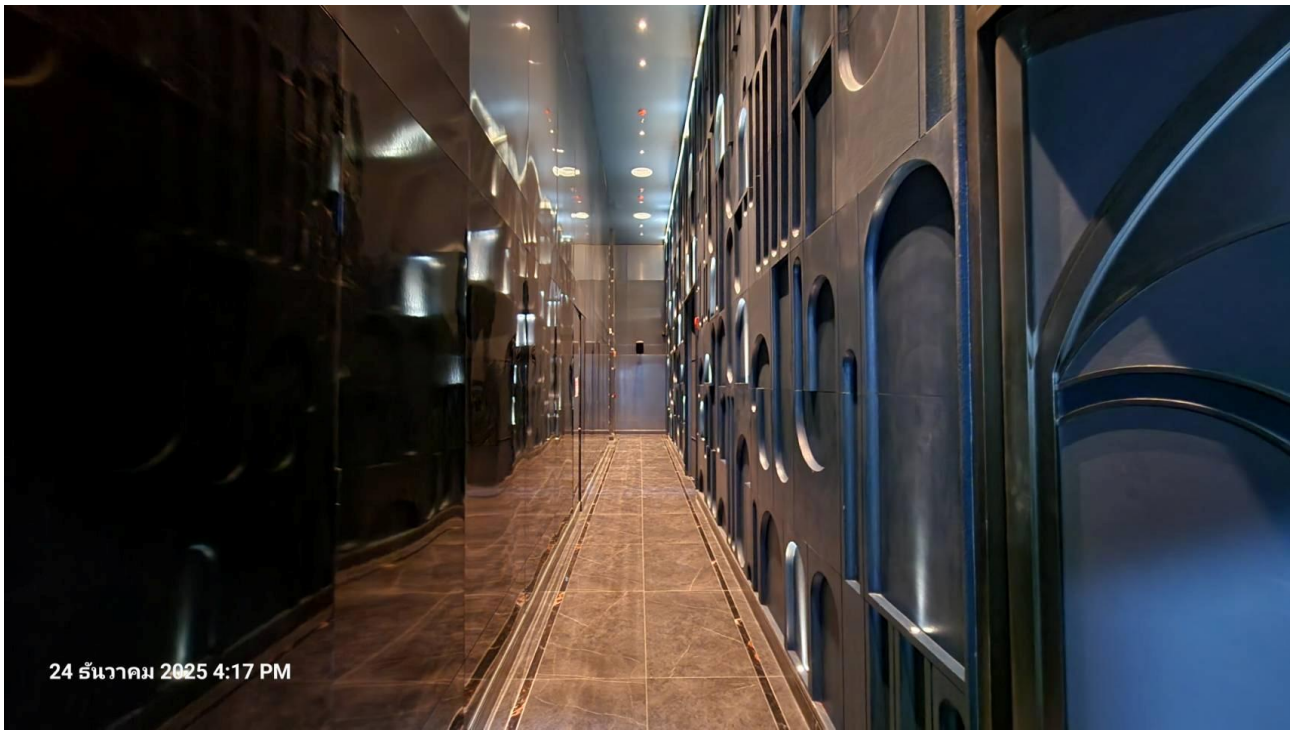

BANGKOK DEC-CON
Public Company Limited

บริษัท บางกอก เดค-คอน จำกัด (มหาชน)
0-2925-5777 0-2925-5778
Admin@bangkokdeccon.com
www.bangkokdeccon.com

Photos of Completed Work
